


COMPLETION PLAN OF TUBEWELL

NAME OF WORK :- CONSTRUCTION OF T.W. LOHAR KHERA G.P W/S SCHEME BLOCK MISHRIKH DISTRICT SITAPUR
 NAME OF PROGRAMME :- J J M - 2
 NAME OF CLIENT :- S.W.S.M. & U.P. JAL NIGAM (R)
 NAME OF TPI :- CEINSYS TECH LIMITED
 CONTRACT AGREEMENT :- 95/ED/2020-21 DT 23 MAR 21
 COVER AGREEMENT :- 115 / ED / PHASE - 2 / 22-23/ VIII...DATED 21 - 09 - 2022
 LOWERED ASSEMBLY CHART OF T.W. OF LOHAR KHERA G.P W/S SCHEME DISTRICT :- SITAPUR

LOWERED ASSEMBLY IN MT.

500 MM DIA BORE

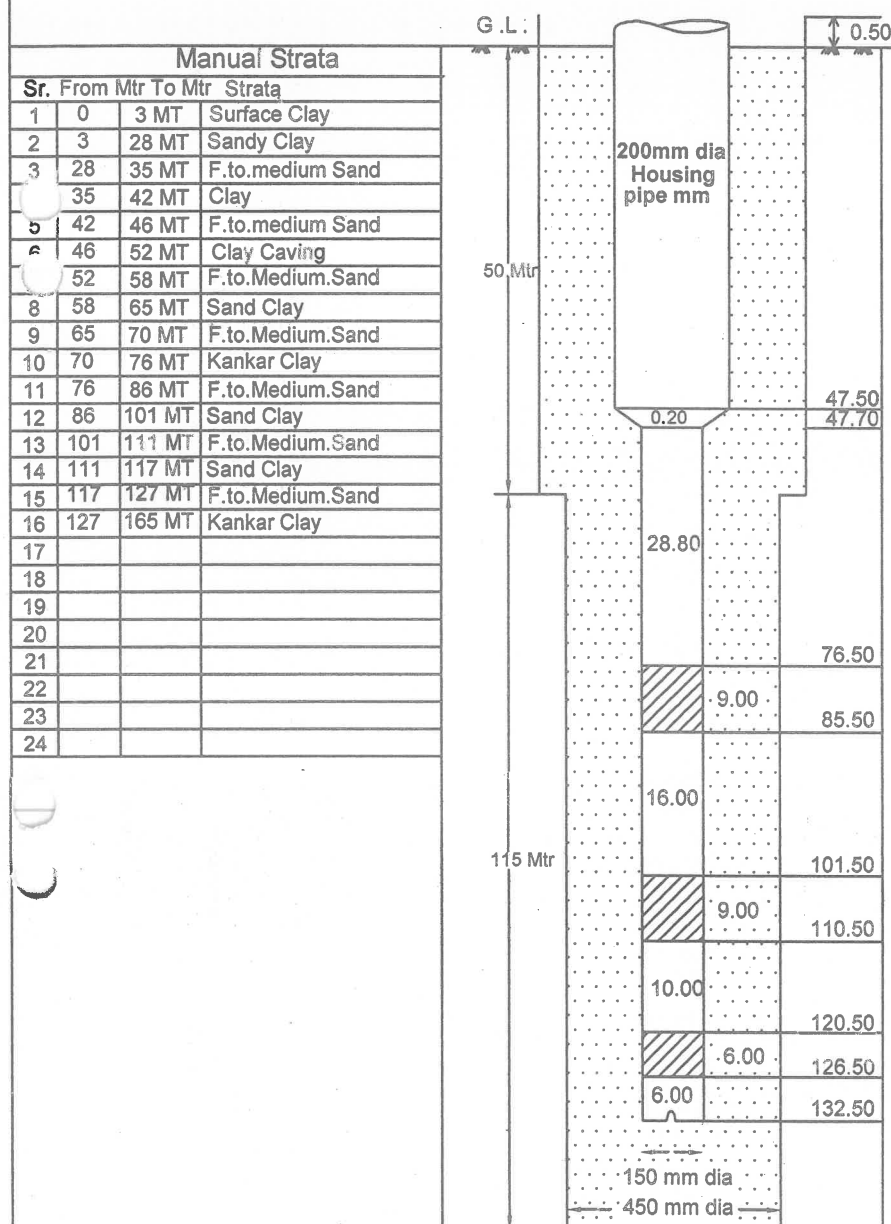

ABSTRACT

1- Required Discharge	:- 560 LPM
2- Static Water Level	:- 10 MTR
3- Type of Rig Machine	:- R.C./D.C
4- Bore Size	:- 500x450 mm dia
5- Assembly size	:- 200x150 mm dia
6- Total Depth of Bore	:- 165 Mtr
a- 600 mm dia o to 50	:- 50.00 m.
b- 200 mm dia 50 to 165	:- 115.00 m.
Total	:- 165.00 m.
7- Logging date	:- 25-11-2022
8- Logging Depth	:- 165.00 m.

LOGGING REPORT

Sr.	Depth Range Mbgl	Thickness m.	Remarks
1	28 - 35	7.00 m	Good
2	42 - 46	4.00 m	Good
3	52 - 58	6.00 m	Good
4	65 - 70	5.00 m	Good
5	76 - 86	10.00 m	Good
6	101 - 111	10.00 m	Good
7	117 - 127	10.00 m	Good
8			Note- No Proper granular Zone in Countered Below 127 M BGL To Till Depth
9			
10			
11			

11- Detail of Tubewell Assembly

(A) 200 mm dia Housing Pipe	:- 48.00 Meter
(B) 200x150 mm dia MS Reducer	:- 0.20 Meter
(C) 150 mm dia MS Plain Pipe	:- 60.80 Meter
(D) 150 mm dia Slotted Pipe	:- 24.00 Meter
Total	:- 133.00 Meter
A G L	:- 0.50 Meter
B G L	:- 132.50 Meter
12- Date of Lowering	25-11-2022

PREPARED BY

RECOMMENDED BY

APPROVED BY

(P. M.)
 LARSEN AND TOUBRO
 LIMITED SITAPUR

(VERIFIED BY)
 (T. P. I.)

(VIKRAM JEET)
 (J E)
 DIVISION OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW

(RAJENDRA KUMAR)
 (A E)
 DIVISION OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW

(SHRI RAM GUPTA)
 EXECUTIVE ENGINEER
 DIVISION OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW
