

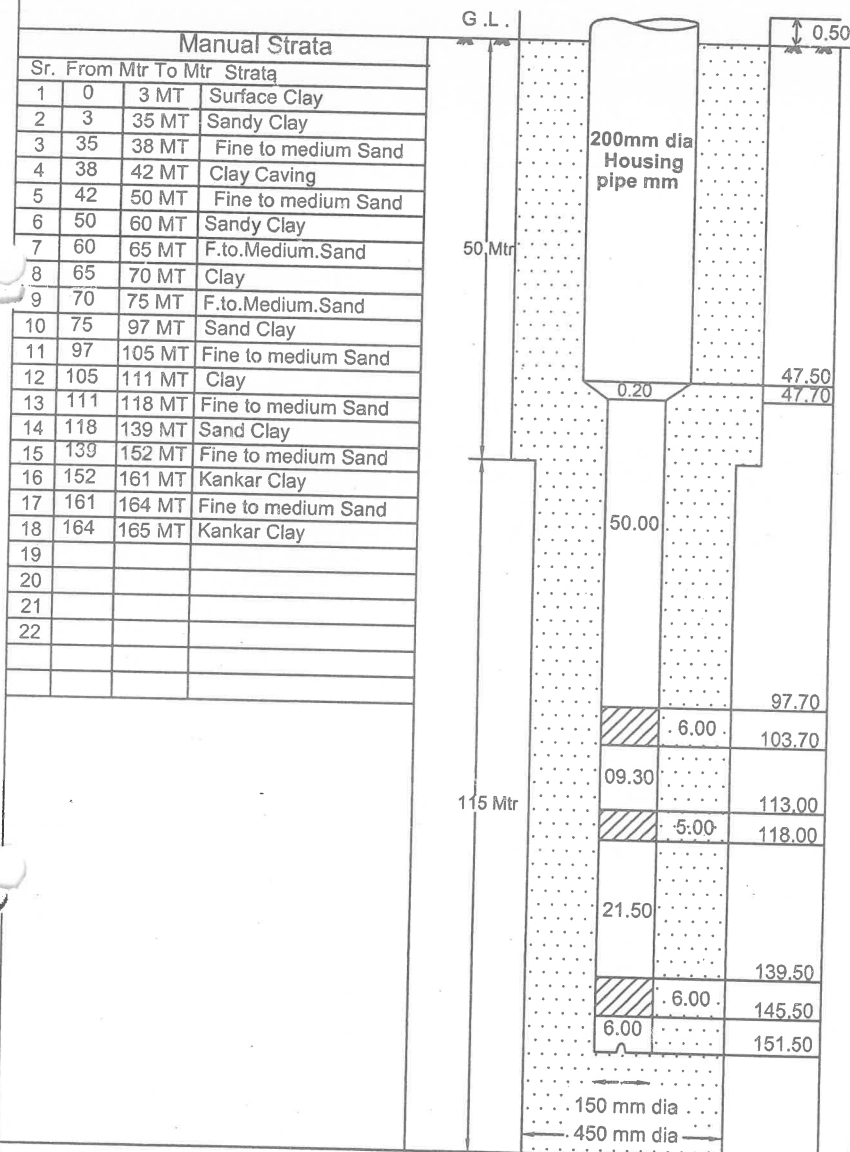
(142)

COMPLETION PLAN OF TUBEWELL

NAME OF WORK :- CONSTRUCTION OF T.W. MADNAPUR G.P W/S SCHEME BLOCK HARGAON DISTRICT SITAPUR
 NAME OF PROGRAMME :- J J M - 2
 NAME OF CLIENT :- S.W.S.M. & U.P. JAL NIGAM (R)
 NAME OF TPI :- CEINSYS TECH LIMITED
 CONTRACT AGREEMENT :- 95/ED/2020-21 DT 23 MAR 21
 COVER AGREEMENT :- 206 /ED/21-22 / III/DATED 08/12/2021
 LOWERED ASSEMBLY CHART OF T.W. OF MADNAPUR G.P W/S SCHEME DISTRICT :- SITAPUR

LOWERED ASSEMBLY IN MT.

500 MM DIA BORE

**ABSTRACT**

1- Required Discharge	:- 440 LPM
2- Static Water Level	:- 08 MTR
3- Type of Rig Machine	:- R.C./D.C
4- Bore Size	:- 500x450 mm dia
5- Assembly size	:- 200x150 mm dtr
6- Total Depth of Bore	:- 165 Mtr
a- 500 mm dia o to 50	:- 50.00 m.
b- 200 mm dia 50 to 165	:- 115.00 m.
Total	:- 165.00 m.
7- Logging date	:- 01-11-2022
8- Logging Depth	:- 165.00 m.

LOGGING REPORT

Sr.	Depth Range Mbgl	Thickness m.	Remarks
1	35 - 38	3.00 m	Good
2	42 - 50	8.00 m	Good
3	60 - 65	5.00 m	Good
4	70 - 75	5.00 m	Good
5	97 - 105	8.00 m	Good
6	111 - 118	7.00 m	Good
7	139 - 152	13.00 m	Good
8	161 - 164	3.00 m	Good
9			Note - SL-6 May Consider As 113 To 118-Mtr.
10			
11			

11- Detail of Tubewell Assembly

(A) 200 mm dia Housing Pipe	:- 48.00 Meter
(B) 200x150 mm dia MS Reducer	:- 0.20 Meter
(C) 150 mm dia MS Plain Pipe	:- 86.80 Meter
(D) 150 mm dia Slotted Pipe	:- 17.00 Meter
Total	:- 152.00 Meter
A G L	:- 0.50 Meter
B G L	:- 151.50 Meter
12- Date of Lowering	:- 02-10-2022

PREPARED BY

[Signature]
 (P.M.)
 LARSEN AND TOUBRO
 LIMITED SITAPUR

RECOMMENDED BY

[Signature]
 (VIKRAM JEET)
 (J E)
 DIVISION OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW

APPROVED BY

[Signature]
 (RAJENDRA KUMAR)
 (A E)
 DIVISION OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW

[Signature]
 (SHRI RAM GUPTA)
 EXECUTIVE ENGINEER
 DIVISION OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW
