


Completion Plan of Aswan Urf Hajiganj-GP Soraon- Block, District- Prayagraj

Agency of construction : LARSEN & TOUBRO LTD  
 Drilling Started On : 13-09-2023  
 Drilling Completed On : 29-10-2023  
 Assembly lowered on : 30-10-2023  
 Size of bore : 600mm $\phi$  from GL to 65m BGL  
 450mm $\phi$  from 65m BGL to 126m BGL  
 Size of tubewell : 300\*150mm  
 Req. Discharge : 760LPM

LOGGING REPORT

Logging Date : 20-09-2023  
 Depth Logged : 106m  
 Directed by : Mr Sanjeet Sharma(Hydrogeologist)  
 (All Geo Solution)  
 STPI,MNIT Campus,Teliarganj

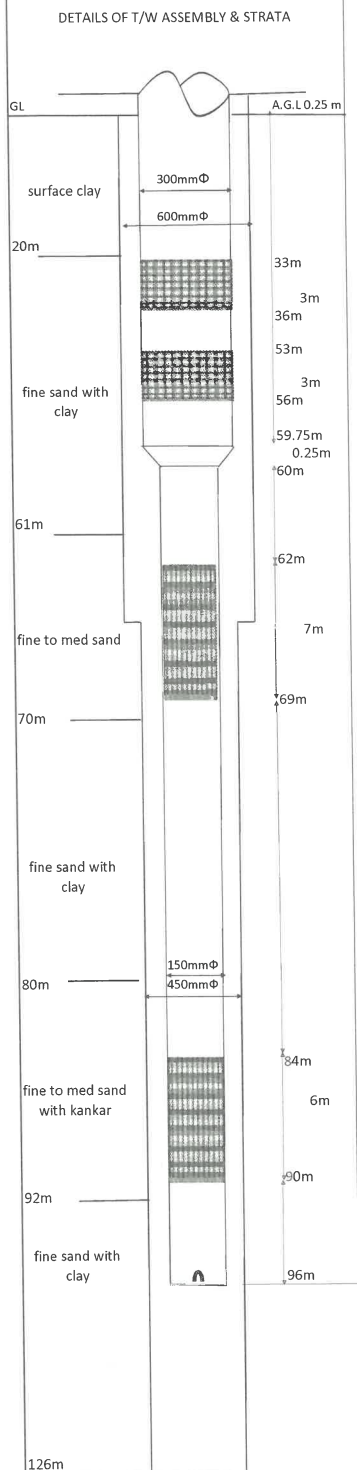

Sr.No	Depth Range in Meter B.G.L	Thickness in Meter	Remarks	Note
1	20-27	7	GOOD	1.All zones are intermixed with thin bands of kankar.
2	32-36	4	GOOD	
3	53-56	3	GOOD	
4	62-69	7	GOOD	
5	84-90	6	GOOD	

T.W Constructed By

Subhankar sil(PM)  
L&T Construction

Vishal Kumar Singh  
MTCPL(TPI)

(Jitendra yadav)  
Junior Engineer

(Karunakar Singh)  
Assistant Engineer

(Syed. Mohd. Shabaz)  
Executive Engineer

Division office E&M,UP Jal Nigam (Rural) Prayagraj
