


COMPLETION PLAN OF TUBEWELL

NAME OF WORK :- CONSTRUCTION OF T.W. MAKHUAPUR G.P W/S SCHEME BLOCK KHAIRABAD DISTRICT SITAPUR
 NAME OF PROGRAMME :- J J M - 2
 NAME OF CLIENT :- S.W.S.M. & U.P. JAL NIGAM (R)
 NAME OF TPI :- CEINSYS TECH LIMITED
 CONTRACT AGREEMENT :- 95/ED/2020-21 DT 23 MAR 21
 COVER AGREEMENT :- 115 / ED / PHASE - 2 / 22-23/ VIII...DATED 21 - 09 - 2022
 LOWERED ASSEMBLY CHART OF T.W. OF MAKHUAPUR G.P W/S SCHEME DISTRICT :- SITAPUR

LOWERED ASSEMBLY IN MT. 600 MM DIA BORE

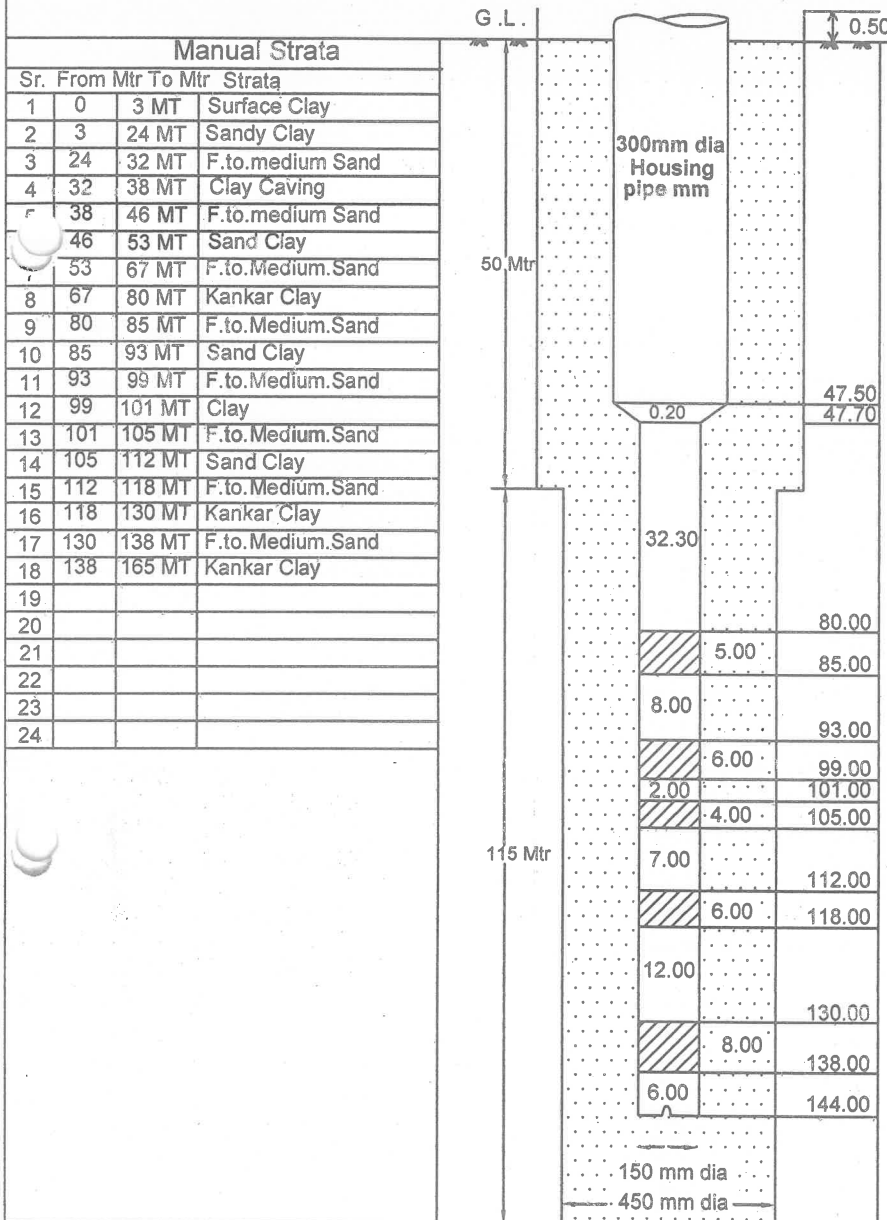

ABSTRACT	
1- Required Discharge	:- 940 LPM
2- Static Water Level	:- 12 MTR
3- Type of Rig Machine	:- R.C./D.C
4- Bore Size	:- 600x450 mm dia
5- Assembly size	:- 300x150 mm dtr
6- Total Depth of Bore	:- 165 Mtr
a- 600 mm dia o to 50	:- 50.00 m.
b- 300 mm dia 50 to 165	:- 115.00 m.
Total	:- 165.00 m.
7- Logging date	:- 06-12-2022
8- Logging Depth	:- 155.00 m. BGL.

LOGGING REPORT

Sr.	Depth Range Mbgl	Thickness m.	Remarks
1	24 - 32	8.00 m	Good
2	38 - 46	8.00 m	Good
3	53 - 67	14.00 m	Good
4	80 - 85	5.00 m	Good
5	93 - 99	6.00 m	Good
6	101 - 105	4.00 m	Good
7	112 - 118	6.00 m	Good
8	130 - 138	8.00 m	Good
9			Note-Sr No-5 to 8 are fine to very fine in nature and are highly kankar inter mix
10			
11			

11- Detail of Tubewell Assembly

(A) 300 mm dia Housing Pipe	:- 48.00 Meter
(B) 300x150 mm dia MS Reducer	:- 0.20 Meter
(C) 150 mm dia MS Plain Pipe	:- 67.30 Meter
(D) 150 mm dia Slotted Pipe	:- 29.00 Meter
Total	:- 144.50 Meter
A G L	:- 0.50 Meter
B G L	:- 144.00 Meter
12- Date of Lowering	07-12- 2022

PREPARED BY

RECOMMENDED BY

APPROVED BY

(P. M.)
 LARSEN AND TOUBRO
 LIMITED SITAPUR

(T. P. I.)
 (VERIFIED BY)

(J. E.)
 (VIKRAM JEET)
 DIVISION OFFICE (E/M)
 U.P. JAL NIGAM (R) LUCKNOW

(A. E.)
 (RAJENDRA KUMAR)
 DIVISION OFFICE (E/M)
 U.P. JAL NIGAM (R) LUCKNOW

(SHRI RAM GUPTA)
 EXECUTIVE ENGINEER
 DIVISION OFFICE (E/M)
 U.P. JAL NIGAM (R) LUCKNOW
