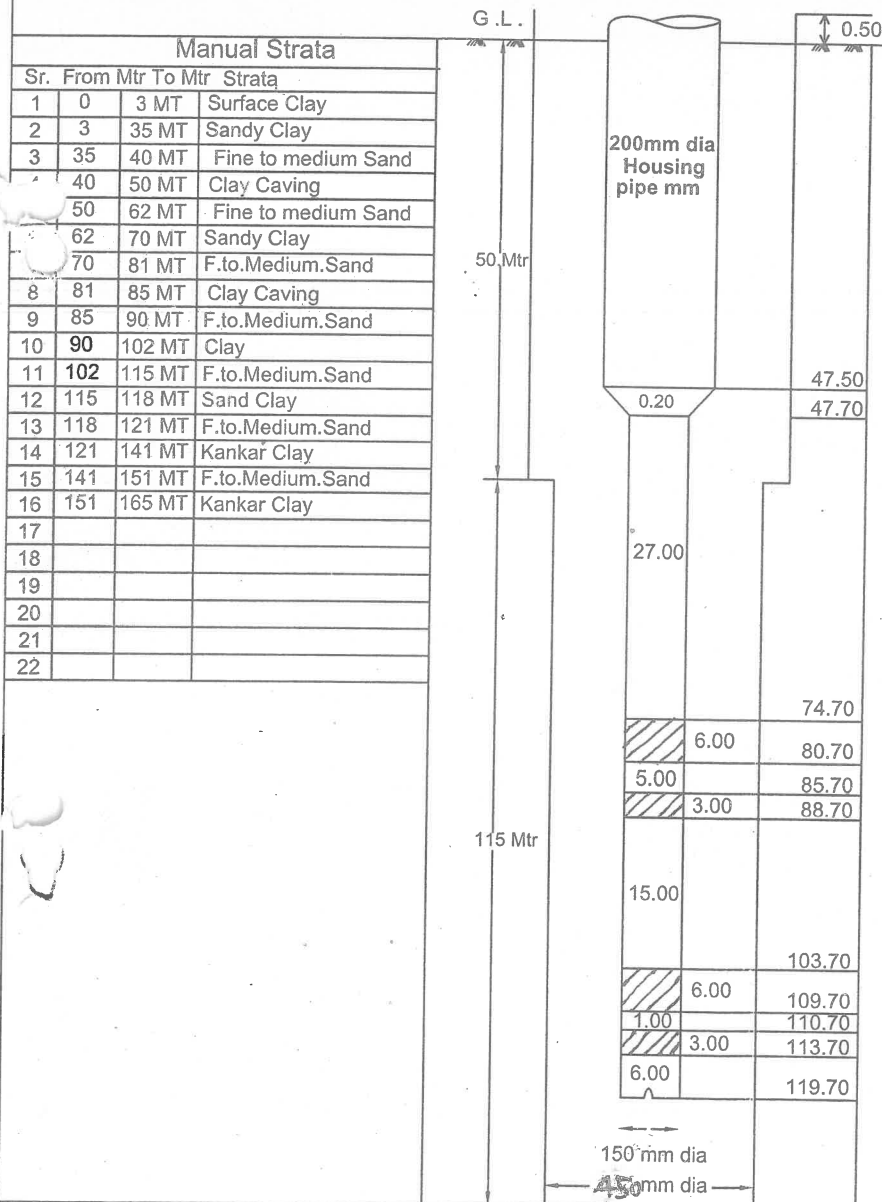


COMPLETION PLAN OF TUBEWELL

NAME OF WORK :- CONSTRUCTION OF T.W. NARA INPUR G.P W/S SCHEME BLOCK MISHRIKH DISTRICT SITAPUR
 NAME OF PROGRAMME :- J J M - 2
 NAME OF CLIENT :- S.W.S.M. & U.P. JAL NIGAM (R)
 NAME OF TPI :- CEINSYS TECH LIMITED
 CONTRACT AGREEMENT :- 95/ED/2020-21 DT 23 MAR 21
 COVER AGREEMENT :- 206/ED/21-22/III / DATE 10.12/2021
 LOWERED ASSEMBLY CHART OF T.W. OF NARA INPUR G.P W/S SCHEME DISTRICT :- SITAPUR

LOWERED ASSEMBLY IN MT. 500 MM DIA BORE

**ABSTRACT**

1-	Required Discharge	:-	420 LPM
2-	Static Water Level	:-	11 MTR
3-	Type of Rig Machine	:-	R.C./D.C
4-	Bore Size	:-	500x450 mm dia
5-	Assembly size	:-	200 x150 mm dtr
6-	Total Depth of Bore	:-	165 Mtr
a-	500 mm dia o to 50	:-	50.00 m.
b-	200 mm dia 50 to 165	:-	115.00 m.
	Total	:-	165.00 m.
7-	Logging date	:-	01-08-2022
8-	Logging Depth	:-	165.00 m.

LOGGING REPORT

Sr.	Depth Range M bgl	Thickness m.	Remarks
1	35 - 40	5.00 m	Good
2	50 - 62	12.00 m	Good
3	70 - 81	11.00 m	Good
4	85 - 90	5.00 m	Good
5	102 - 115	13.00 m	Good
6	118 - 121	3.00 m	Good
7	141 - 151	10.00 m	Good
8			
9			
10			

11- Detail of Tubewell Assembly

(A)	200 mm dia Housing Pipe	:-	48.00 Meter
(B)	200x150 mm dia MS Reducer	:-	0.20 Meter
(C)	150 mm dia MS Plain Pipe	:-	54.00 Meter
(D)	150 mm dia Slotted Pipe	:-	18.00 Meter
	Total	:-	120.20 Meter
	A G L	:-	0.50 Meter
	B G L	:-	119.70 Meter
12-	Date of Lowering	:-	04-08-2022

PREPARED BY

 ARSEN & TOUBRO LIMITED
 LARSEN AND TOUBRO
 LIMITED SITAPUR

(VERIFIED BY)
 (T.P.I)

RECOMMENDED BY

 (VIKRAM JEET)
 (J E)
 DIVISIONAL OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW


 (DINESH KUMAR)
 (A E)
 DIVISIONAL OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW

APPROVED BY

 (SHRI RAM GUPTA)
 EXECUTIVE ENGINEER
 DIVISIONAL OFFICE (E/M)
 U.P JAL NIGAM (R) LUCKNOW
