


(200)

COMPLETION PLAN OF TUBEWELL

NAME OF WORK :- CONSTRUCTION OF T.W. PADARKHA G.P W/S SCHEME BLOCK AILLIYA DISTRICT SITAPUR
 NAME OF PROGRAMME :- JJM-2
 NAME OF CLIENT :- S.W.S.M. & U.P. JAL NIGAM (R)
 NAME OF TPI :- CEINSYS TECH LIMITED
 CONTRACT AGREEMENT :- 95/ED/2020-21 DT 23 MAR 21
 COVER AGREEMENT :- 106/ED/21-22/ DATED 10-08-2022
 LOWERED ASSEMBLY CHART OF T.W. OF PADARKHA G.P W/S SCHEME DISTRICT :- SITAPUR

LOWERED ASSEMBLY IN MT. 600 MM DIA BORE

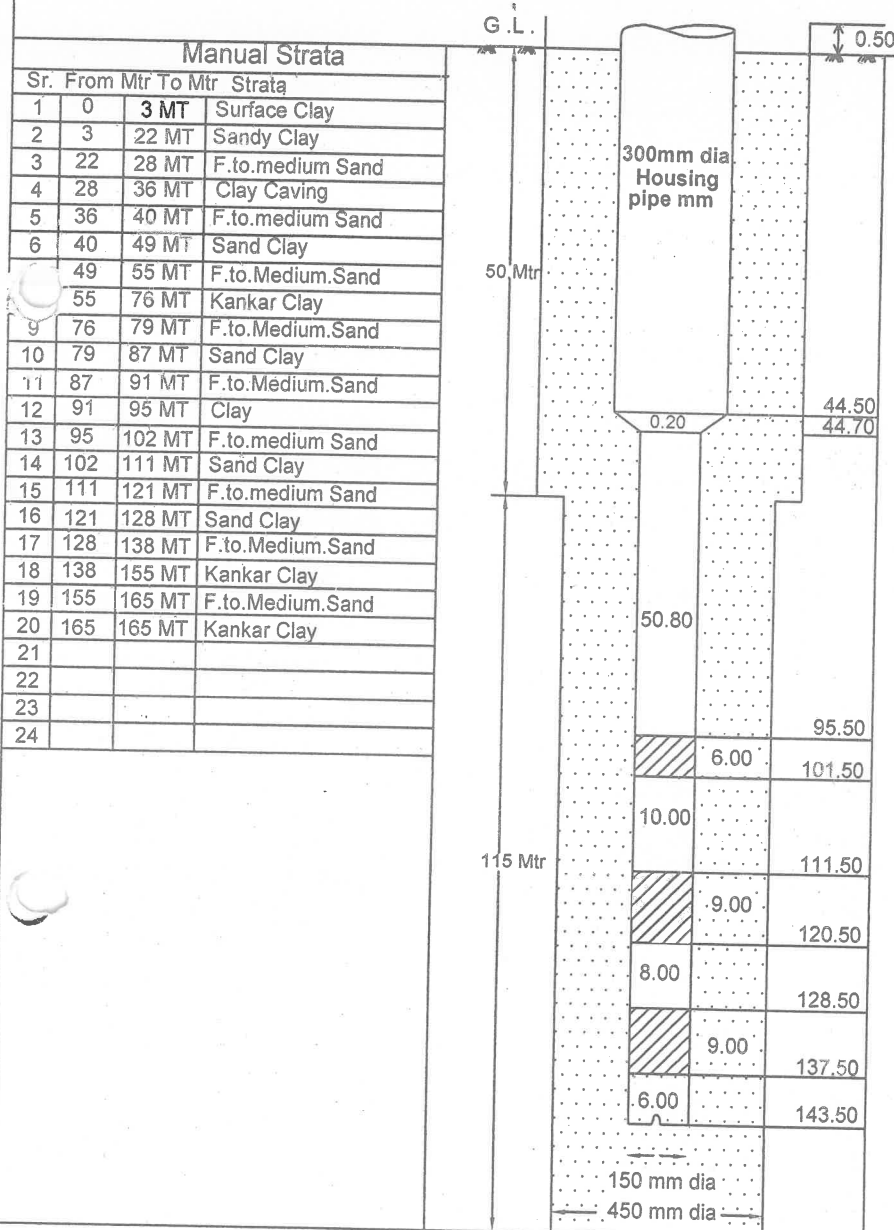

ABSTRACT	
1- Required Discharge	:- 610 LPM
2- Static Water Level	:- 08 MTR
3- Type of Rig Machine	:- R.C./D.C
4- Bore Size	:- 600x450 mm dia
5- Assembly size	:- 300x150 mm dtr
6- Total Depth of Bore	:- 165 Mtr
a- 600 mm dia o to 50	:- 50.00 m.
b- 300 mm dia 50 to 165	:- 115.00 m.
Total	:- 165.00 m.
7- Logging date	:- 19-12-2022
8- Logging Depth	:- 165.00 m. BGL.

LOGGING REPORT

Sr.	Depth Range Mbgl	Thickness m.	Remarks
1	22 - 28	7.00 m	Good
2	36 - 40	4.00 m	Good
3	49 - 55	6.00 m	Good
4	76 - 79	3.00 m	Good
5	87 - 91	4.00 m	Good
6	95 - 102	7.00 m	Good
7	111 - 121	10.00 m	Good
8	128 - 138	10.00 m	Good
9	155 - 165	10.00 m	Good
10			
11			

11- Detail of Tubewell Assembly	
(A) 300 mm dia Housing Pipe	:- 45.00 Meter
(B) 300x150 mm dia MS Reducer	:- 0.20 Meter
(C) 150 mm dia MS Plain Pipe	:- 74.80 Meter
(D) 150 mm dia Slotted Pipe	:- 24.00 Meter
Total	:- 144.00 Meter
A G L	:- 0.50 Meter
B G L	:- 143.50 Meter
12- Date of Lowering	21-12-2022

PREPARED BY

RECOMMENDED BY

APPROVED BY

(P.M.)
LARSEN AND TOUBRO
LIMITED SITAPUR

(VERIFIED BY)
(T.P.I.)

(VIKRAM JEET)
(J E)
DIVISION OFFICE (E/M)
U.P. JAL NIGAM (R) LUCKNOW

(RAJENDRA KUMAR)
(A E)
DIVISION OFFICE (E/M)
U.P. JAL NIGAM (R) LUCKNOW

(SHRI RAM GUPTA)
EXECUTIVE ENGINEER
DIVISION OFFICE (E/M)
U.P. JAL NIGAM (R) LUCKNOW
