


Completion Plan of Basana Khas-Jamua -GP , Pratappur- Block, District- Prayagraj

DETAILS OF T/W ASSEMBLY & STRATA

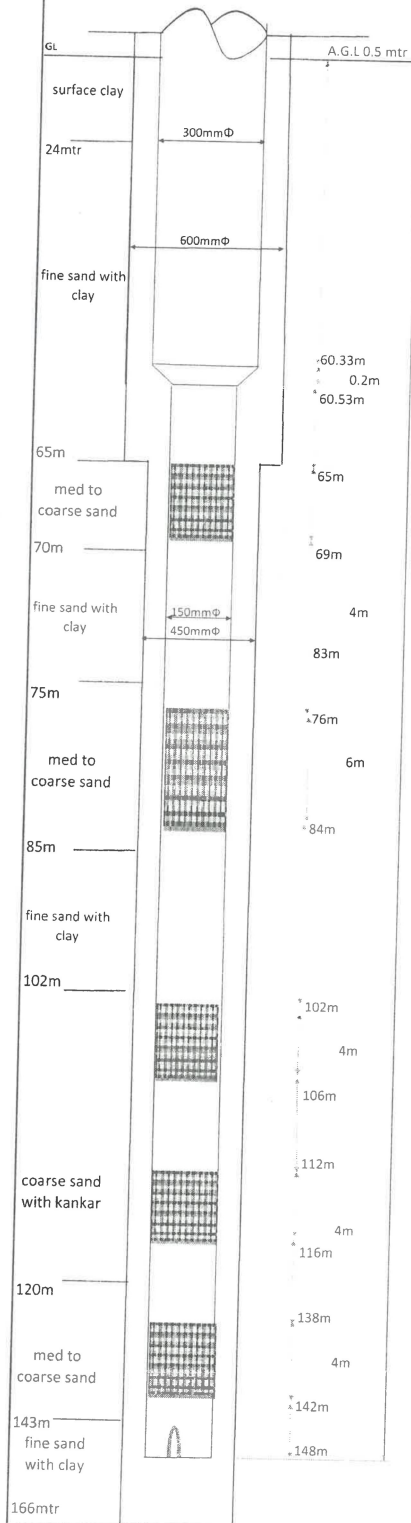

Agency of construction : LARSEN & TOUBRO LTD
 Drilling Started On : 17-05-2023
 Drilling Completed On : 29-05-2023
 Assembly lowered on : 30-05-2023
 Size of bore : 600mmφ from GL to 65m BGL
 450mmφ from 65m BGL to 166m BGL
 Size of tubewell : 300*150 mm
 Req. Discharge : 740 LPM

LOGGING REPORT

Logging report Date : 29-05-2023
 Drilled Depth : 166mtr
 Depth Logged : 166mtr
 Directed by : Dr.S.SHUKLA
 MANAGER(GROUND WATER)
 U.P.JN-LUCKNOW

Sl.No	Depth Range in Meter B.G.L	Thickness in Meter	Remarks	Note
1	54-60	6	GOOD	All zones intermixed with thin bands of kankar.
2	65-69	4	GOOD	
3	76-84	8	GOOD	
4	102-106	4	GOOD	
5	112-116	4	GOOD	
6	138-142	4	GOOD	
7	148-152	4	GOOD	
8	156-166	10	GOOD	

T.W Constructed By

Subhankar sil(PM)
L&T Construction

Sanjay paswan

(Suresh Bhardwaj)
Junior Engineer

(Karunakar Singh)
Assistant Engineer

(Syed. Mohd. Shabaz)
Executive Engineer

Division office E&M,UP Jal Nigam (Rural) Prayagraj
