


Completion Plan of Garhawa_Pure Khudi_Hariharpur-GP,Saidabad- Block, District- Prayagraj

Agency of construction : LARSEN & TOUBRO LTD
 Drilling Started On : 30-09-2023
 Drilling Completed On : 06-10-2023
 Assembly lowered on : 07-10-2023
 Size of bore : 600mmφ from GL to 65m BGL
 450mmφ from 65m BGL to 141m BGL
 Size of tubewell : 300*150mm
 Req. Discharge : 880LPM

LOGGING REPORT

Logging Date : 06-10-2023
 Depth Logged : 134m
 Directed by : Mr Sanjeet Sharma(Hydrogeologist)
 (All Geo Solution)
 STPI, MNIT Campus, Teliarganj
 UPIN-Prayagraj

DETAILS OF T/W ASSEMBLY & STRATA

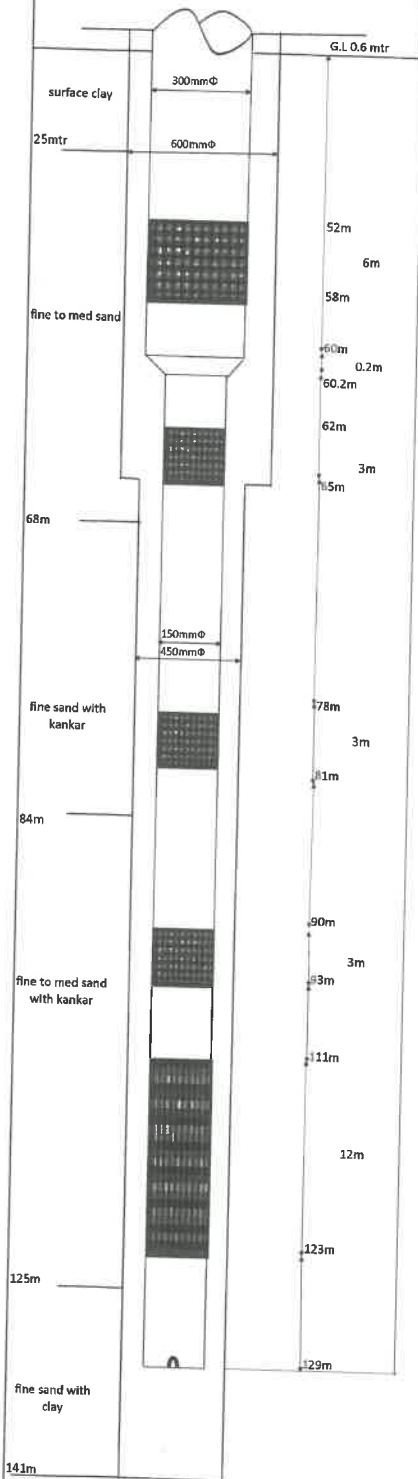

Sl.No	Depth Range in Meter B.G.L	Thickness in Meter	Remarks	Note
1	34-37	3	GOOD	1.All zone are intermixed with thin bands of kankar.
2	52-65	13	GOOD	
3	78-81	3	GOOD	
4	90-93	3	GOOD	
5	111-124	13	GOOD	

T.W Constructed By

Subhankar sil(PM)
 L&T Construction

Sanjay Paswan
 MTCP(LTPI)

(Bandana)
 Junior Engineer(SWSM)

(Karnakar Singh)
 Assistant Engineer

(Syed. Mohd. Shabaz)
 Executive Engineer
