

2024

January 10
Wednesday

Name of Scheme - Mahagourang Block - Lar
Name of Agency - LC INPVT LTD (Nalanda) Phase - 2
Drilling/Lowering - 142/130M • Bore Size - 675 X 500 mm
Tubewell Assembly Size - 300 X 150 mm • Recommended discharge - 800 LPM
Logging date - 13/04/2024, Date of Lowering -

Logging Report :-


- (1) 24 - 28 - 04M
- (2) 31 - 38 - 07M
- (3) 41 - 45 - 04M
- (4) 48 - 55 - 07M
- (5) 59 - 63 - 04M
- (6) 66 - 70 - 04M
- (7) 82 - 89 - 07M
- (8) 93 - 102 - 09M
- (9) 116 - 120 - 04M

125.35 M

AGL(+) - 0.50M

Total lowering - 125.85 M

February, 2024

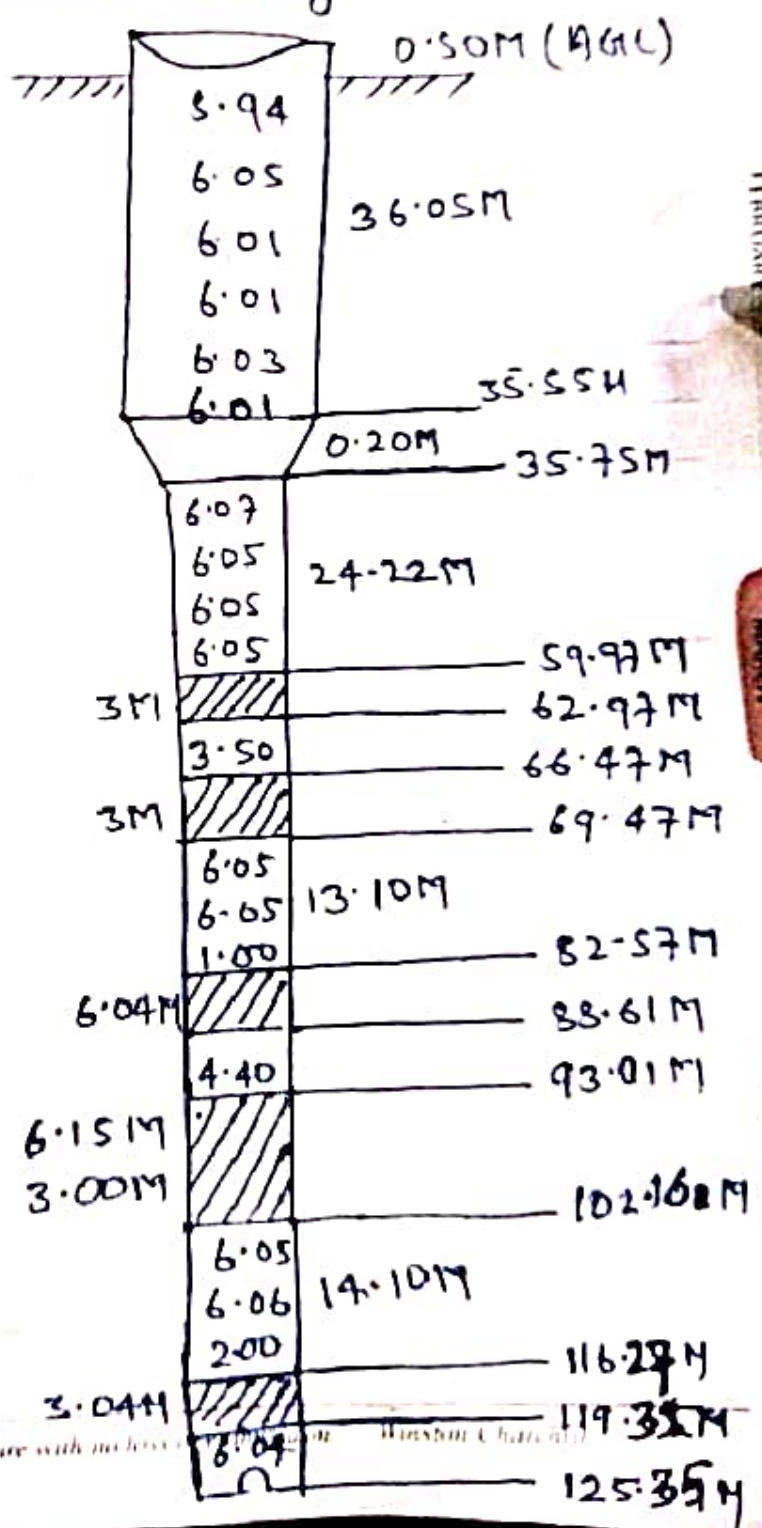

Mon	Tue	Wed	Thu	Fri	Sat	Sun
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30	31				
