




मेधा

Medha Techno Concept Pvt. Ltd.

PMPL-BRCCPL JOINT VENTURE
JAL JEEVAN MISSION PROJECTS, PRATAPGARH, U.P.



Har Ghar Jal
Jal Jeevan Mission

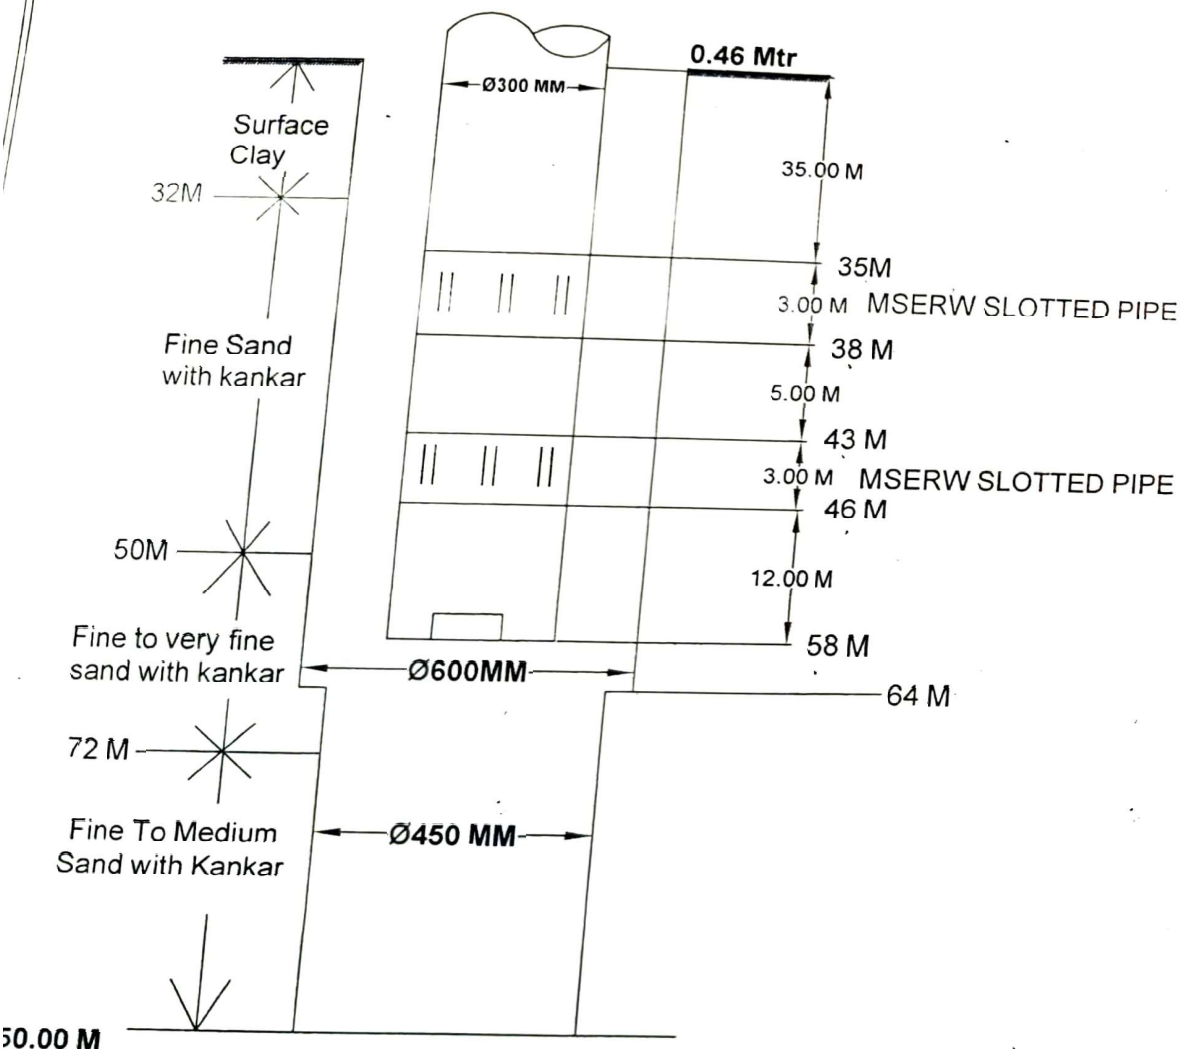

Actual Tubewell Assembly Lowering Chart

1	DISTRICT : PRATAPGARH
2	BLOCK : SADAR
3	VILLAGE : SARAIBEERBHARA Tw No-1
4	DATE OF LOGGING : 02-Jan-2023
5	DATE OF LOWERING : 06-01-2023
6	SIZE OF ASSEMBLY : Ø 300 mm x Ø 300 mm
7	SIZE OF BORE GL to 64 Mbgl - Ø600mmxØ600mm 64 Mtr to 150Mbgl - Ø450mmxØ450mm
8	Required Discharge as per BQ/D : 325 Lpm
9	Proposed/Design Discharge as per Strata : 325 Lpm
10	LOGGING DEPTH : 150.00 Mtr
11	LOGGING BY : <u>ALL Geo Solution</u>
12	MSERW SLOTTED PIPES : 06 Mtr. @ 300 MM

~LOGGING REPORT~

SR. NO.	DEPTH RANGE	THICKNESS (M)	WATER QUALITY
1	35 - 38	03	GOOD
1	43 - 46	03	GOOD
2			

NOTE: 1 Both are fine Sand intermixed with thin band of kankar.

2. The formation water is saline below 74 mbgl to till depth logged.

LOGGING REPORT VERIFIED BY GAURAV SHUKLA (ASST. HYDRO. CIRCLE OFFICE E & M
UP JAL NIGAM (RURAL), PRAYAGRAJ

CLIENT :
STATE WATER SANITATION MISSION
(NAMAMI GANGE & RURAL WATER SUPPLY DEPARTMENT)
GOVERNMENT OF UTTAR PRADESH

PROJECT : PRATAPGARH GROUP OF VILLAGES WATER
SUPPLY SCHEME

EPC CONTRACTOR : PMPL - BRCCPL JOINT VENTURE



	NAME	SIGN	TITLE :	SCALE :
DRWN	Amit Ranjan		PROPOSED TUBE WELL ASSEMBLY	
DSGN			LOWERING DRAWING	
CHKD			GP: Saraibeerbhara	
APPD			WATER SUPPLY SCHEME	
DATE			SHEET NO.	SIZE A4
				REV R0
