


Medhraj Techno Concept Pvt. Ltd.

PMPL-BRCCPL JOINT VENTURE
JAL JEEVAN MISSION PROJECTS, PRATAPGARH, U.P.



Har Ghar Jal
Jal Jeevan Mission

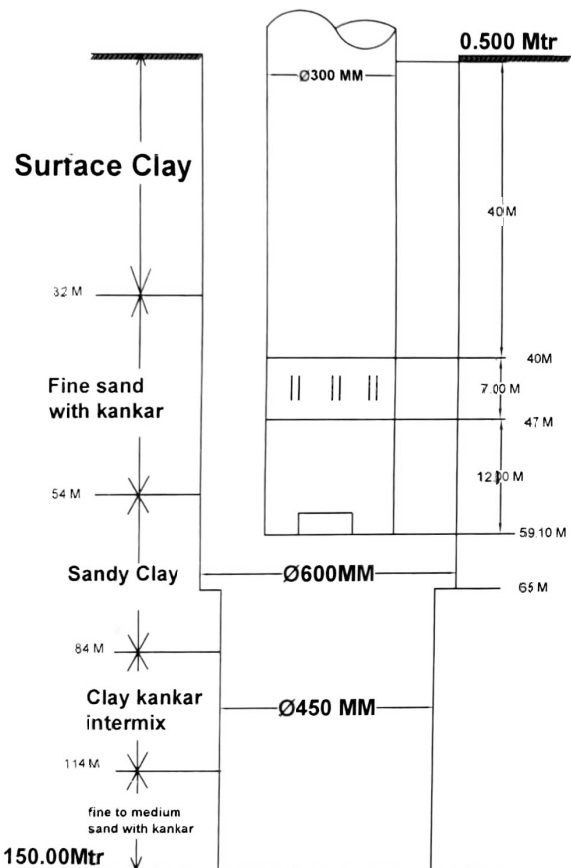

Actual Tubewell Assembly Lowering Chart

PMPL BRCCPL JV

TPIA

JE

AE

EE

1	DISTRICT	Pratapgarh
2	BLOCK	SADAR
3	VILLAGE	Sarai Beerbhadra tw-02
4	DATE OF LOGGING	20.01.2023
5	DATE OF LOWERING	31.01.2023
6	SIZE OF ASSEMBLY	Ø300mm x Ø300mm
7	SIZE OF BORE	
8	REQUIRED DISCHARGE	325 LPM
9	LOGGING DEPTH	119.00Mtr
10	LOGGING BY	Gro Instruments & Techniques
11	USERW SLOTTED PIPES	7.00 Mtr

LOGGING REPORT

SR NO.	DEPTH RANGE	THICKNESS(M)	WATER QUALITY
1	40-47	7	GOOD

NOTE:

1. Quality of ground water is deteriorating Marginal to saline below 56 Mtr bgl to till depth Logged.
2. Please ensure Pre-monsoon water level before lowering the well assembly

LOGGING REPORT VERIFIED BY GAURAV SHUKLA (ASST. HYDRO. CIRCLE OFFICE E & M UP JAL NIGAM (RURAL), PRAYAGRAJ)

CLIENT :
STATE WATER SANITATION MISSION
(NAMAM GANGE & RURAL WATER SUPPLY DEPARTMENT)
GOVERNMENT OF UTTAR PRADESH

PROJECT : PRATAPGARH GROUP OF VILLAGES WATER
SUPPLY SCHEME

EPC CONTRACTOR : PMPL - BRCCPL JOINT VENTURE



	NAME	SIGN	TITLE	SCALE
DRWN	Amit Ranjan		PROPOSED TUBE WELL ASSEMBLY LOWERING DRAWING WATER SUPPLY SCHEME	
DSGN				
CHKD				
APPD				
DATE	-----			
DRAWING NO.	-----			
		SHEET NO. 1 OF 1	SIZE A1	REV R0
