


Medhaji Techno Concept Pvt. Ltd.

PMPL-BRCCPL JOINT VENTURE
JAL JEEVAN MISSION PROJECTS, PRATAPGARH, U.P.



Hār Ghar Jal
Jal Jeevan Mission

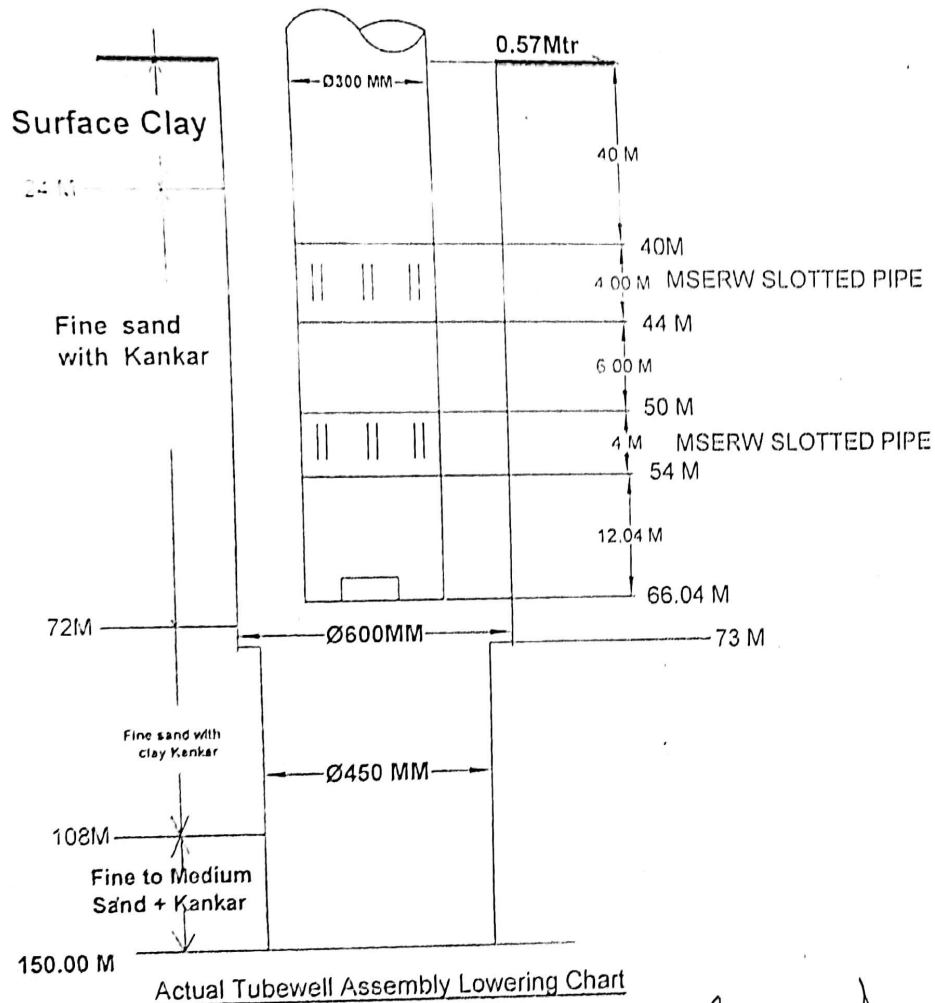

1	DISTRICT PRATAPGARH
2	BLOCK JALJEEVAN
3	VILLAGE BAHMAN
4	DATE OF LOGGING 17.11.2022
5	DATE OF LOWERING 17.11.2022
6	SIZE OF ASSEMBLY Ø 300 mm x Ø 300 mm
7	SIZE OF SCOPE
8	CL. 73 M, 108 M, 150 M
9	73 M, 108 M, 150 M
10	LOGGING DEPTH 150 M
11	LOGGING BY GEO. INSTRUMENTS & TECHNIQUE
12	LOGGING BY SURVEYING INSTRUMENTS & TECHNIQUE

SR NO	DEPTH RANGE	THICKNESS M	WATER QUALITY
1	27-33	6	GOOD
1	40-44	4	GOOD
2	50-54	4	GOOD

NOTE: 1. Fine bands of kankar are intermixed with almost all the zones.
2. Quality of ground water is deteriorating marginal to saline below 60 m bgl to till depth logged.

LOGGING REPORT VERIFIED BY GAURAV SHUKLA (ASST HYDRO. OFFICE E & M UP JAL NIGAM (RURAL) PRAYAGRAJ)

CLIENT
STATE WATER SANITATION MISSION
(NAMAMI GANGE & RURAL WATER SUPPLY DEPARTMENT)
GOVERNMENT OF UTTAR PRADESH

PROJECT : PRATAPGARH GROUP OF VILLAGES WATER SUPPLY SCHEME

EPC CONTRACTOR : PMPL - BRCCPL JOINT VENTURE



	NAME	SIGN	TITLE	SCALE
DRWN	Amit Ranjan		PROPOSED TUBE WELL ASSEMBLY LOWERING DRAWING (UP BAHMAN WATER SUPPLY SCHEME)	
DSGN				
CHKD				
APPD				



DATE: _____ SHEET NO: 1 OF 1
DRAWING NO: _____ SIZE: A4 REV: R0
