


ACTUAL / FINAL ASSEMBLY CHART OF TUBEWELL

NAME OF SCHEME - JAL JEEVAN MISSION
NAME OF SITE - ANTAPUR (BLOCK - SANDALPUR)
NAME OF COMPANY - VSAIPPL - SCL (JV)
TYPE OF RIG/M/C - DC

DISTRICT - KANPUR DEHAT
SIZE OF ASSEMBLY - (200 X 150) mm.
SIZE OF BORE - (500 X 450) mm.
DISCHARGE : 600 LPM

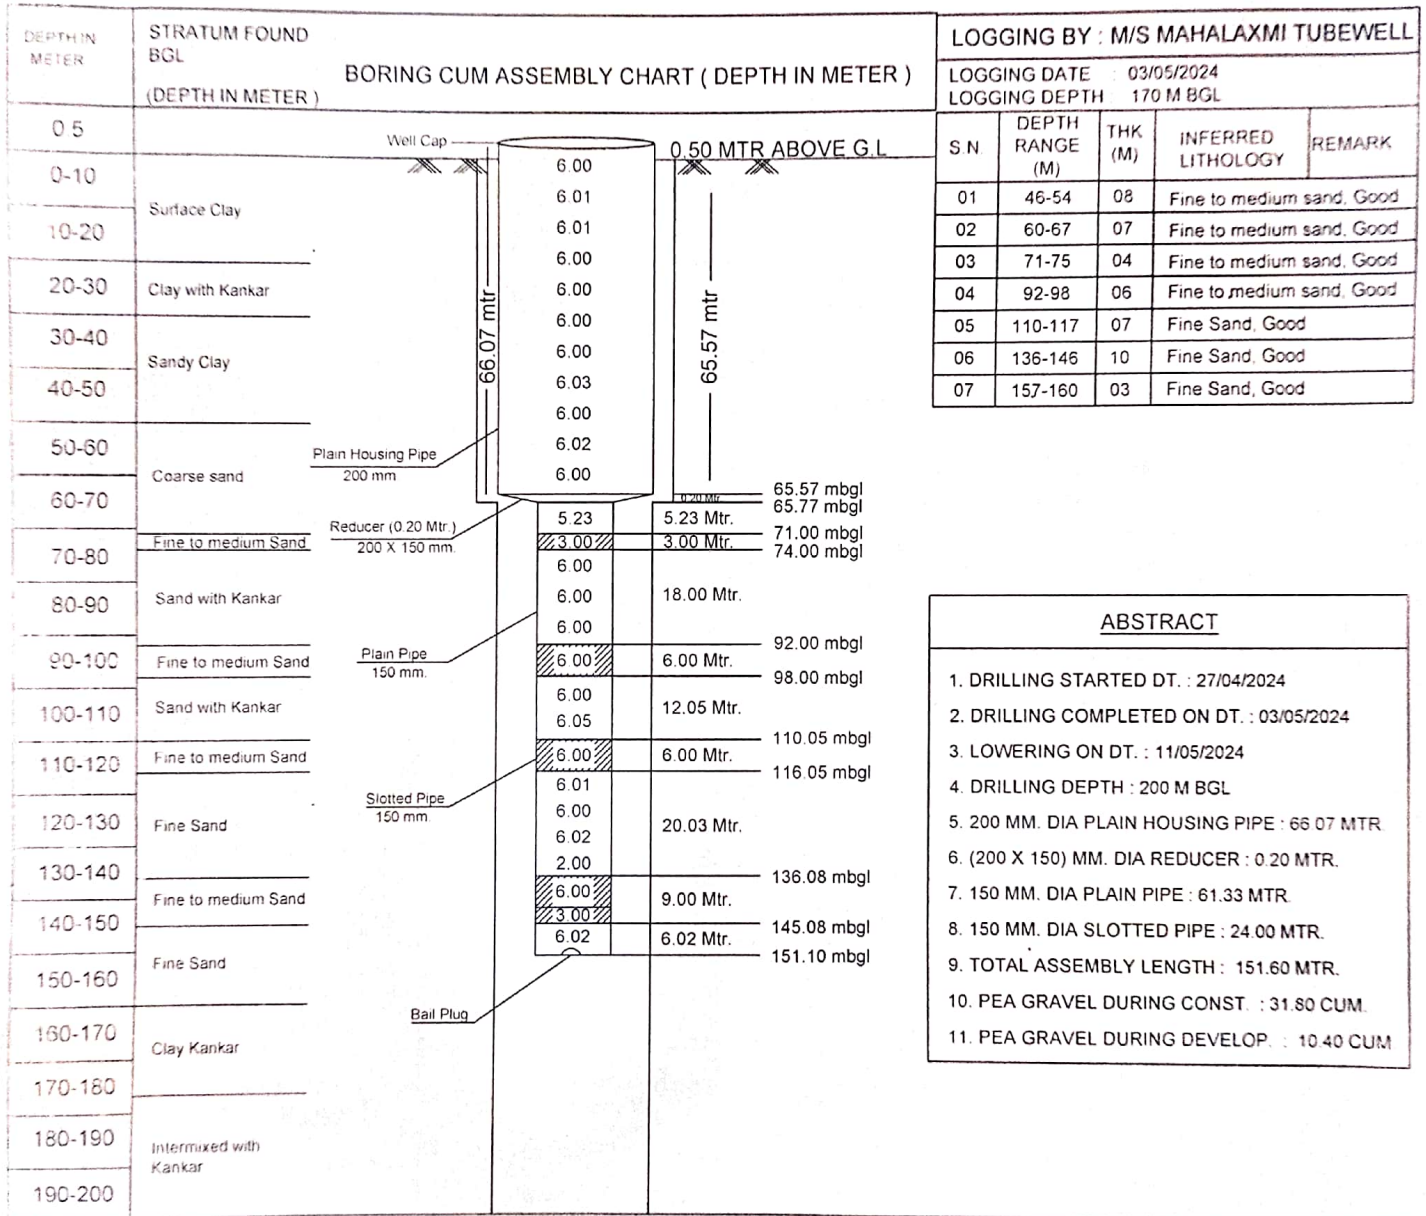

ABSTRACT

1. DRILLING STARTED DT. : 27/04/2024
2. DRILLING COMPLETED ON DT. : 03/05/2024
3. LOWERING ON DT. : 11/05/2024
4. DRILLING DEPTH : 200 M BGL
5. 200 MM. DIA PLAIN HOUSING PIPE : 66.07 MTR.
6. (200 X 150) MM. DIA REDUCER : 0.20 MTR.
7. 150 MM. DIA PLAIN PIPE : 61.33 MTR.
8. 150 MM. DIA SLOTTED PIPE : 24.00 MTR.
9. TOTAL ASSEMBLY LENGTH : 151.60 MTR.
10. PEA GRAVEL DURING CONST. : 31.80 CUM.
11. PEA GRAVEL DURING DEVELOP. : 10.40 CUM



CHECKED BY

JUNIOR ENGINEER

RECOMMEND BY

TPI (BLG)

APPROVED BY

ASSISTANT ENGINEER

EXECUTIVE ENGINEER (E&M)
