


मेधाज

Medha Techno Concept Pvt. Ltd.

PMPL-BRCCPL JOINT VENTURE
JAL JEEVAN MISSION PROJECTS, PRATAPGARH, U.P.



Har Ghar Jal
Jal Jeevan Mission

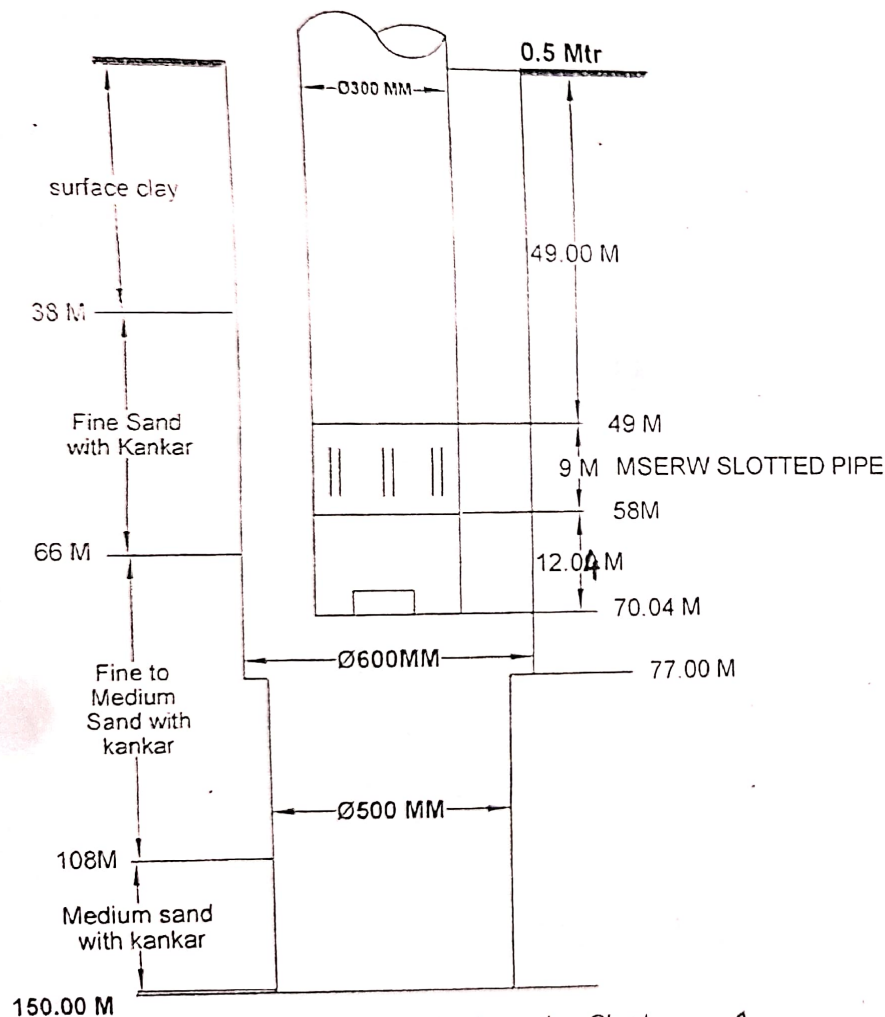

Actual Tubewell Assembly Lowering Chart

1	DISTRICT PRATAPGARH
2	BLOCK SANDANACHANDRIKA
3	VILLAGE SHYAPUR
4	DATE OF LOGGING 22-01-2023
5	DATE OF LOWERING 22-01-2023
6	SIZE OF ASSEMBLY 300mm x 300mm
7	SIZE OF BORE
8	SL. NO. 1 NO. 2 NO. 3 NO. 4 NO. 5
9	11 Mtr 12 Mtr 13 Mtr 14 Mtr 15 Mtr
10	LOGGING DEPTH 14.00 M
11	LOGGING BY DRD INSTRUMENT & TECHNIQUE
12	LOGGING BY DRD INSTRUMENT & TECHNIQUE

SP	DEPTH	THICKNESS	WATER
NO	RANGE	(M)	QUALITY
1	40-50	10	Good

NOTE: 1. Fine bands of kankar are intermixed with above said zone below 67 M to 70 M depth logged water quality marginal to saline.
2. Please ensure pre-monsoon water level before lower the well assembly.

LOGGING REPORT VERIFIED BY CAURAV SHUKLA, ASST. HYDRO. DRDLE OFFICE 2 & 4 M UP JAL NIGAM (RURAL), PRAYAGRAH

CLIENT: STATE WATER SANITATION MISSION
(NAMAMI GANGE & RURAL WATER SUPPLY DEPARTMENT)
GOVERNMENT OF UTTAR PRADESH

PROJECT: PRATAPGARH GROUP OF VILLAGES WATER
SUPPLY SCHEME

EPC CONTRACTOR: PMPL - BRCCPL JOINT VENTURE



	NAME	SIGN	TITLE	SCALE
DRWN	Amit		PROPOSED TUBE WELL ASSEMBLY	
DSGN			LOWERING DRAWING	
CHKD			GP Pratanagar	
APPD			WATER SUPPLY SCHEME	
DATE				
DRAWING NO.				
			SHEET NO 1 OF 1	SIZE A4 REV R0

PMPL BRCCPL JV

TPIA

JE

AE

EE

