

POWER MECH
Growth Unlimited

Mechanical Techno Concept Pvt. Ltd.

PMPL-BRCPL JOINT VENTURE JAL JEEVAN MISSION PROJECTS, PRATAPGARH, U.P.



Har Char Jal
Jal Jeevan Mission



1. DISTRICT: PRATAPGARH
2. BLOCK: SANGPUR
3. VILLAGE: BHAYANIGARH
4. DATE OF LOGGING: 10-11-2022
5. DATE OF LOWERING: 12-11-2022
6. SIZE OF ASSEMBLY: Ø 300 mm x Ø 300 mm
7. SIZE OF BORE: Ø 102 mm x Ø 50 mm
8. Required Discharge as per BOD: 550 Lpm
9. Proposed Design Discharge as per State: 400 Lpm
10. LOGGING DEPTH: 150.00 Mtr
11. LOGGING BY: ALL GEO SOLUTIONS
12. MSERW SLOTTED PIPES: Ø8 MM x 300 MM

LOGGING REPORT -

S.R.	DEPTH NO. RANGE	THICKNESS (M)	WATER QUALITY
1	26-30	4	GOOD
2	42-45	3	GOOD
3	81 - 87	6	GOOD

NOTE: 1. S/N No 1 & 2 are finer in nature and are highly kankar intermixed

2. The formation water quality deteriorating from marginal to saline below 144 Mbgl to till depth logged

LOGGING REPORT VERIFIED BY GAURAV SHUKLA (ASST. HYDRO. CIRCLE OFFICE E & M
UP JAL NIGAM (RURAL), PRAYAGRAH)

CLIENT: STATE WATER SANITATION MISSION
(NAMAMI GANGE & RURAL WATER SUPPLY DEPARTMENT)
GOVERNMENT OF UTTAR PRADESH

PROJECT: PRATAPGARH GROUP OF VILLAGES WATER
SUPPLY SCHEME


EPC CONTRACTOR: PMPL - BRCPL JOINT VENTURE



NAME	SIGN	TITLE	SCALE
DRWN: Anil Ranjan		PROPOSED TUBE WELL ASSEMBLY LOWERING DRAWING UP BHAYANIGARH WATER SUPPLY SCHEME	N B S
DSGN: CHKD: APPD:			

DATE	SHEET NO.	SIZE	REV
	1 OF 1	A4	R3

Actual Tubewell Assembly Lowering Chart

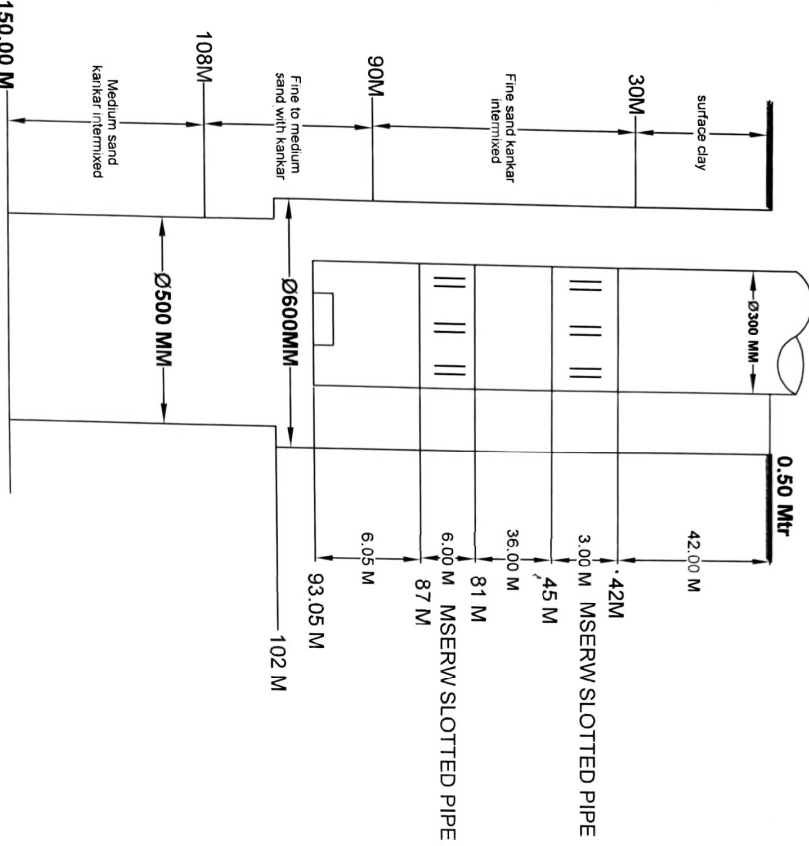

PMPL BRCPL JV

TP/A

JE

AE

EE
