


मेधज
Medhaj Techno Concept Pvt. Ltd.

PMPL-BRCCPL JOINT VENTURE
JAL JEEVAN MISSION PROJECTS, PRATAPGARH, U.P.

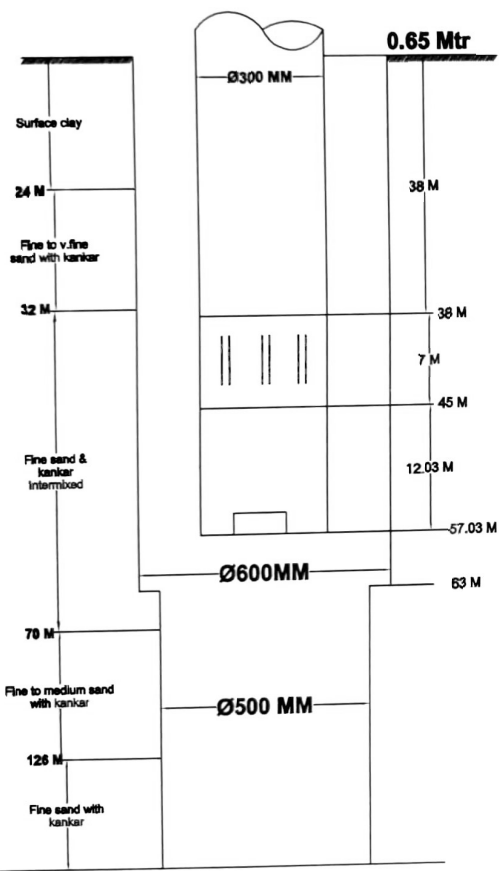

Actual Tubewell Assembly Lowering Chart

PMPL BRCCPL JV

TPIA

JE

AE

EE

1.	DISTRICT : Pratapgarh
2.	BLOCK :SANGIPUR
3.	VILLAGE :Amra & Semra
4.	DATE OF LOGGING : 05 - 12 - 2022
5.	DATE OF LOWERING : 10- 12 - 2022
6.	SIZE OF ASSEMBLY : Ø300mm x Ø300mm
7.	SIZE OF BORE : GL to 63 Mbgl - Ø600mm x Ø600mm 63 Mtr to 150 Mbgl - Ø500mm x Ø500mm
8.	Required discharge as per BOQ : 700 LPM
9.	Proposed/ Design discharge as per strata: 300 LPM
10.	LOGGING DEPTH : 150 Mbgl
11.	LOGGING BY : All Geo Solutions.
12.	MSEW SLOTTED PIPES : 7.00 Mtr

-LOGGING REPORT-

SR NO.	DEPTH RANGE	THICKNESS	WATER QUALITY
1.	24 - 28	4	GOOD
2.	38 - 45	7	GOOD

NOTE:

1. The formation water quality is deteriorating below 52mbgl to till depth logged.
2. Sr. No. 1 and 2 interbed with thin bands of kankar.

LOGGING REPORT VERIFIED BY GAURAV SHUKLA (ASST. HYDRO. CIRCLE OFFICE E & M UP JAL NIGAM (RURAL), PRAYAGRAJ)

CLIENT : STATE WATER SANITATION MISSION
(NAMAMI GANGE & RURAL WATER SUPPLY DEPARTMENT)
GOVERNMENT OF UTTAR PRADESH

PROJECT : PRATAPGARH GROUP OF VILLAGES WATER
SUPPLY SCHEME

EPC CONTRACTOR : PMPL - BRCCPL JOINT VENTURE



NAME	SIGN	TITLE :	SCALE :
DRWN	Amit Ranjan	PROPOSED TUBE WELL ASSEMBLY LOWERING DRAWING WATER SUPPLY SCHEME GP - Semra	N W E S
DSGN			
CHKD			
APPD			
DATE		SHEET NO. 1 OF 1	SIZE A4
DRAWING NO.			REV R0
