



KALPA-TARU

aarvee associates
architects engineers & consultants pvt. ltd.



QUALITY MANAGEMENT SYSTEM

Format No :
KPTL/232221F/00023


DEPTH OF STARTA

PROPOSED ASSEMBLY DETAILS

Block- Jaithara.
GP- Tigra Bhamara.

SL.	DPR Details -
	Lowering Date - <u>21/08/2023.</u>
1	Water Discharge in LPM - <u>630</u>
2	Bore well Drilling dia- <u>600,500mm</u>
3	Bore well Drilling depth- <u>120 MTR.</u>

LOGGING REPORT

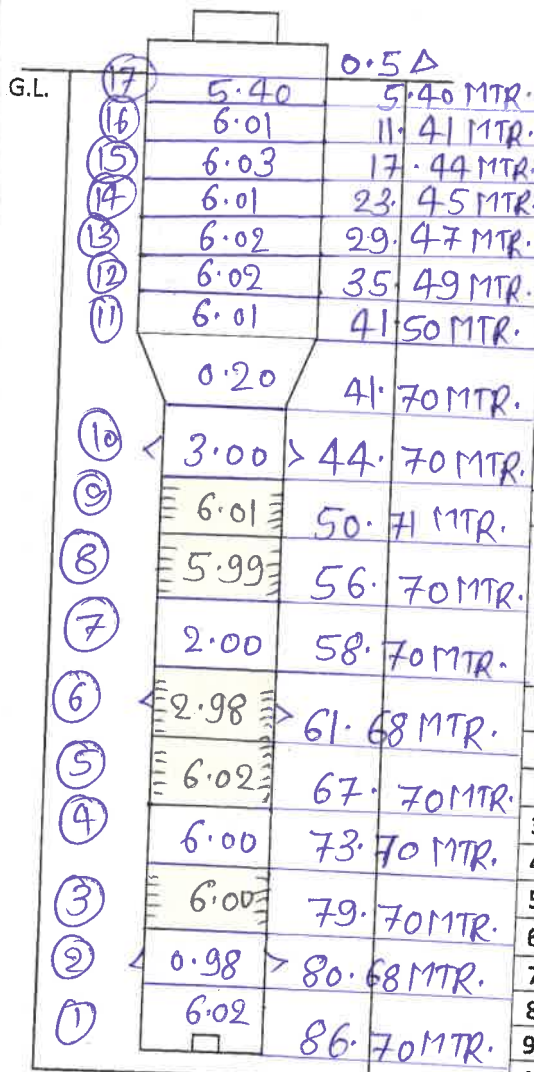

Depth-	Date-		
SL.	Depth Range	Thickness	Remarks
1			
2			
3			
4			
5			
6			
7			
8			
9			
10			
11			

Assembly Details

Proposed Assembly for Lowering

1.	300mm dia MS Plain Pipe-	42.00 MTR.
2.	200mm dia MS Plain Pipe	18.00 MTR.
3.	200mm dia MS Slotted Pipe-	27.00 MTR.
4.	200mm dia LCG Pipe -	-
5.	300/200 mm dia Reducer -	01 nos.
6.	MS Bail Plug-	01 nos.
7.	MS Ring 300mm-	06 nos.
8.	MS Ring 200mm-	09 nos.
9.	MSSI Clamp-	01 nos.
10.	Centre Guide -	01 nos.
11.	TW Assembly Support-	01 nos.
12.	MS Well Cap	01 nos.
13.	Pea Gravel Packing-	01 nos.

Supul Kumar.
KPTL

TPI

CLIENT (UPJN)

Lowering work executed as per assembly chart.
