



QUALITY MANAGEMENT SYSTEM

Format No : KPTL/232221F/00023


DEPTH OF STARTA

PROPOSED ASSEMBLY DETAILS

Block- Jaitheera
GP- Nagla Painsi Ud Khairulji

SL.	DPR Details -	29/9/2023
	Lowering Date -	380 Lpm
1.	Water Discharge in LPM -	500 m
2.	Bore well Drilling dia-	110 mtr
3.	Bore well Drilling depth-	

LOGGING REPORT

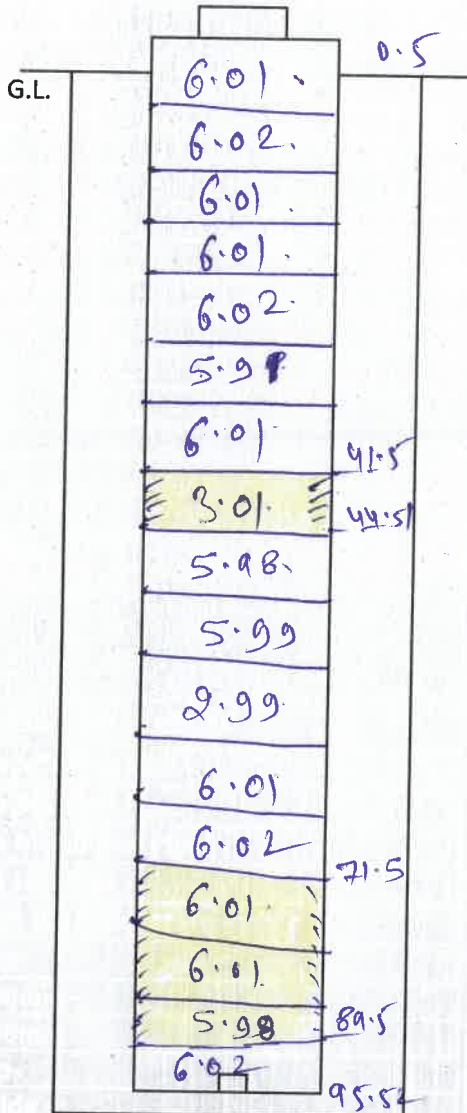

$$\text{Total} = 95.52 + 0.5$$

$$= 96.02$$

Depth-	Date-		
SL.	Depth Range	Thickness	Remarks
1			
2			
3			
4			
5			
6			
7			
8			
9			
10			
11			

Assembly Details

Proposed Assembly for Lowering

1.	300mm dia MS Plain Pipe-	
2.	200mm dia MS Plain Pipe	75.01
3.	200mm dia MS Slotted Pipe-	21.01
4.	200mm dia LCG Pipe -	
5.	300/200 mm dia Reducer -	
6.	MS Bail Plug-	01
7.	MS Ring 300mm-	
8.	MS Ring 200mm-	16
9.	MSSI Clamp-	01
10.	Centre Guide -	03
11.	TW Assembly Support-	01
12.	MS Well Cap -	01
13.	Pea Gravel Packing-	27.67 cu

KPTL
[Signature]

TPI
Lowering work executed as per assembly chart.

CLIENT (UPJN)
