


TUBEWELL'S DRILLING AND LOWERING DETAILS

1	Project	:	Survey Design, Preparation of DPR, Construction, Commissioning, Testing & O&M for 10 years of Various Rural Water Supply Projects for Distt. Sambhal.
2	Client	:	M/s State Water & Sanitation Mission (SWSM) Uttar Pradesh
3	Contractor	:	M/s NKG Infrastructure Ltd., New Delhi
4	Name of Gram Panchayat	:	Dharampur Ratta
5	Name of Block	:	Baniyakhera
6	Name of District	:	Sambhal
7	Size of tubewell	:	200 X 150 mm dia

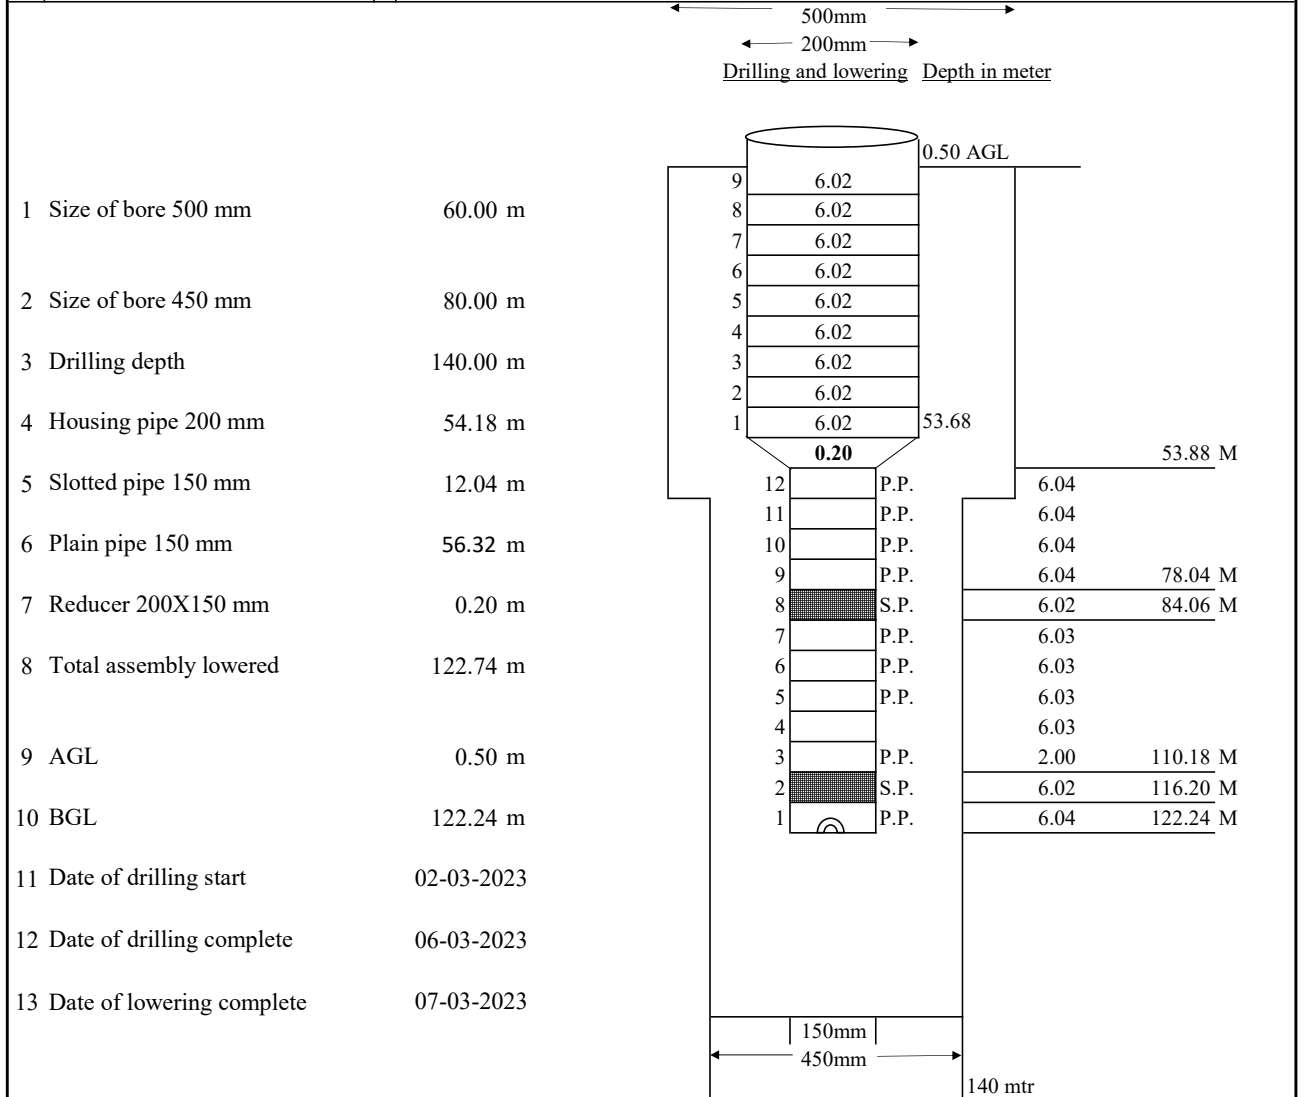

Logging Report

1	34	m	to	40	m	6.00	m	-	Good (Fine To Medium Sand)
2	40	m	to	50	m	10.00	m	-	Good (Medium Sand)
3	67	m	to	75	m	8.00	m	-	Good (Medium Sand With Kankar)
4	75	m	to	92	m	17.00	m	-	Good (Medium Sand)
5	108	m	to	118	m	10.00	m	-	Good (Medium Sand)
6	129	m	to	136	m	7.00	m	-	Good (Medium Sand)
