PROJECTS (INDIA) LIMITED

QUALITY MANAGEMENT SYSTEM
IMC/232221F/00023

DEPTH OF STRATA

PROPOSED ASSEMBLY DETAILS

Dastampur (Nidhouli kalan)

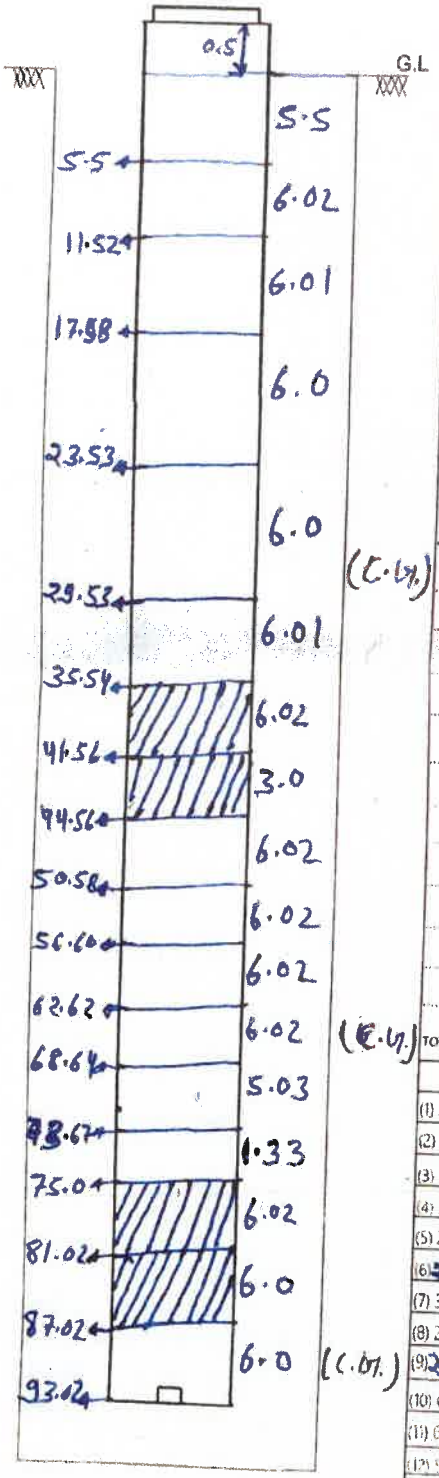

SL	DPR DETAILS-		
	Lowering Date	06/03/2023	
1	Water Discharge in LPM	380 LPM	
2	Bore well Drilling	110 mtr	
3	Drilling Depth 500MM Dia-	110m	600MM Dia-
4	Tube Well Assembly		
5	400MM Dia	200MM Dia	150MM Dia
6		✓	

1.- LOGGING REPORT

Depth Logged- MBGL | Date of Logging:

SL	Depth Range MBGL	Thickness in Mtr	Remarks
1	35 - 45	10	
2			
3	75 - 87	12	
4			
5			
6			
7			
8			
9			
10			
11			

ASSEMBLY DETAILS

200 MM m.m Dia Housing Pipe A.G.L 0.5M m

..... m.m Dia Housing Pipe ..... m

..... m.m Dia Reducer Pipe ..... to ..... m

..... m.m Dia ..... Pipe ..... to ..... m

..... m.m Dia ..... Pipe ..... to ..... m

..... m.m Dia ..... Pipe ..... to ..... m

..... m.m Dia ..... Pipe ..... to ..... m

..... m.m Dia ..... Pipe ..... to ..... m

..... m.m Dia ..... Pipe ..... to ..... m

..... m.m Dia ..... Pipe ..... to ..... m

..... m.m Dia ..... Pipe ..... to ..... m

..... m.m Dia ..... Pipe ..... to ..... m

..... m.m Dia ..... Pipe ..... to ..... m

TOTAL ASSEMBLY= ..... m+ A.G.L(m)= ..... m

3.- Proposed Assembly for Lowering

(1) 300MM DIA MSERW PLAIN PIPE =

(2) 200 MM DIA MSERW PLAIN PIPE = 71.98m

(3) 150MM DIA MSERW PLAIN PIPE =

(4) 300/150 MM DIA REDUCER =

(5) 200/150 MM DIA REDUCER =

(6) 200MM DIA MSERW SLOTTED PIPE = 21.04

(7) 300 MM DIA WELL CAP =

(8) 200MM WELL CAP = 1

(9) 200MM DIA CENTER GUIDE = 3

(10) GRAVEL PACKING =

(11) 600 MM DIA BORE DIGGING = 18.644 Cum

(12) 500 MM DIA BORE DIGGING =

TOTAL ASSEMBLY = 0.5M + 93.02 = 93.52M

JMC

TPI

CLIENT (UPJN)

Lowering work executed as per assembly chart
