KALPA-TARU | aarvee associates

QUALITY MANAGEMENT SYSTEM
Format No : KPTL/232221F/00023

DEPTH OF STARTA

PROPOSED ASSEMBLY DETAILS

Block- Mathura

GP- kutaina mafi

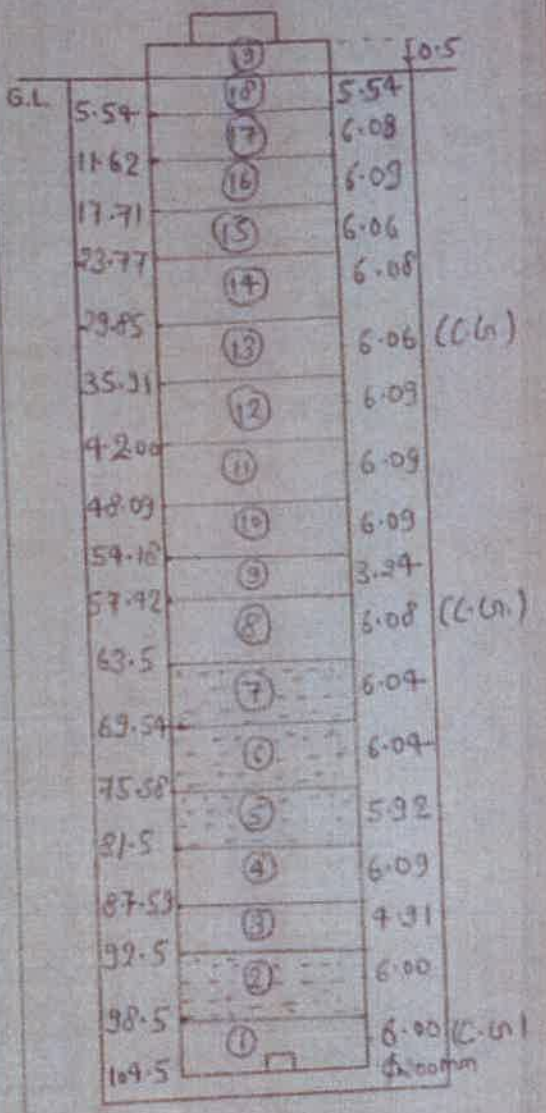

SL	DPR Details -
	Lowering Date- 3/05/2023
1	Water Discharge in LPM - 450
2.	Bore well Drilling dia- 500mm
3.	Bore well Drilling depth- 110 mtr

LOGGING REPORT

Depth- Date-

SL	Depth Range	Thickness	Remarks
1	63-82	19	
2	88-103	15	
3			
4			
5			
6			
7			
8			
9			
10			
11			

Assembly Details

Proposed Assembly for Lowering

1. 300mm dia MS Plain Pipe-	
2. 200mm dia MS Plain Pipe -	81.00 mtr.
3. 200mm dia MS Slotted Pipe-	24.00 mtr.
4. 200mm dia LCG Pipe -	
5. 300/200 mm dia Reducer -	
6. MS Bail Plug-	1
7. MS Ring 300mm-	
8. MS Ring 200mm-	17
9. MSSI Clamp-	
10. Centre Guide -	3
11. TW Assembly Support-	
12. MS Well Cap -	1
13. Pea Gravel Packing-	

Shubham
KPTL

TPI
Lowering work executed as per assembly chart

CLIENT (UPJN)
