JMC PROJECTS (INDIA) LIMITED

QUALITY MANAGEMENT SYSTEM

JMC/232221F/00023 R2

DEPTH OF STRATA

PROPOSED ASSEMBLY DETAILS

UP- Sirsa tippu (marhera)

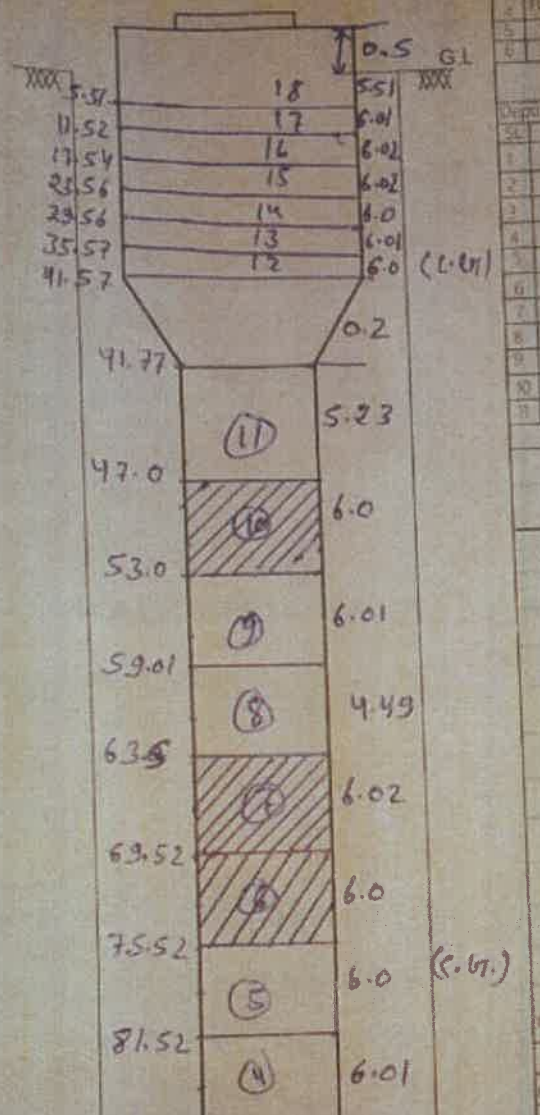


| | | | |
|---|---|---|---|
| | DPR DETAILS | | |
| SL | Lowering Date | 03/03/2023 | |
| 1 | Water Discharge in LPM | 760 LPM | |
| 2 | Bore Well Drilling | 120 mtr. | |
| 3 | Drilling Depth 300MM Dia | 75M | 600MM Dia 45M |
| 4 | Tube Well Assembly | | |
| 5 | 300MM Dia | 200MM Dia | 150MM Dia |
| 6 | ✓ | ✓ | |

## 1.- LOGGING REPORT

| Depth Logged MBGL | | Date of Logging | |
|---|---|---|---|
| SL | Depth Range MBGL | Thickness in Mtr | Remarks |
| 1 | 47-53 | 06M | |
| 2 | | | |
| 3 | 60-77 | 17M | |
| 4 | | | |
| 5 | 85-100 | 15M | |
| 6 | | | |
| 7 | | | |
| 8 | | | |
| 9 | | | |
| 10 | | | |
| 11 | | | |

## ASSEMBLY DETAILS

m.m Dia Housing Pipe A.G.L 0.5M m

m.m Dia Housing Pipe m

m.m Dia Reducer Pipe to m

m.m Dia Pipe to m

m.m Dia Pipe to m

m.m Dia Pipe to m

m.m Dia Pipe to m

m.m Dia Pipe to m

m.m Dia Pipe to m

m.m Dia Pipe to m

m.m Dia Pipe to m

m.m Dia Pipe to m

m.m Dia Pipe to m

TOTAL ASSEMBLY = m+ A.G.L(m) = m

## 3.- Proposed Assembly for Lowering

(1) 300MM DIA MSERW PLAIN PIPE = 42.07M

(2) 200 MM DIA MSERW PLAIN PIPE = 33.75M

(3) 150MM DIA MSERW PLAIN PIPE =

(4) 300/200 MM DIA REDUCER = 1, length (0.2M)

(5) 200/150 MM DIA REDUCER =

(6) 200MM DIA MSERW SLOTTED PIPE = 30.02M

(7) 300 MM DIA WELL CAP = 1

(8) 200MM WELL CAP =

(9) 200MM DIA CENTER GUIDE = 3.

(10) GRAVEL PACKING = 2219.32 Cum.

(11) 600 MM DIA BORE DIGGING =

(12) 500 MM DIA BORE DIGGING =

TOTAL ASSEMBLY = 0.5+41.57+63.77+0.2=10

TPI

CLIENT (UPJN)

SHOT ON REDMI 7
AI DUAL CAMERA

lowering work executed as per assembly chart
