Completion Plan of Tubewell

NAME OF WORKS : Construction of T/W of G.P- SIHULI PARSA WSS , Block-MITHAURA, District- MAHARAJGANJ

NAME OF CLIENT : S.W.S.M. & U.P. JAL NIGAM (R)

NAME OF TPI : Medhaj Techno Concept Pvt Ltd

CONTRACT AGREEMENT NO : 18/ED/Phase-3/2021-22 dated 07.01.2022

COVER AGREEMENT NO : 486/ED/PHASE-3/ 2022-23/XI Dt- 27/02/2023

Lowered Assembly chart of T/W of G.P-SIHULI PARSA W/S Scheme, Block-MITHOURA, District-MAHARAJGANJ

S. No	Depth (m bgl) From (Mtr)	To (Mtr)	Stratum
1	No of MS Ring		
2	200 mm dia		5.00
3	150 mm Dia		21
4			
5	Well Cap		
6	200mm dia		1 Nos
7	Ball Plug		
8	150 mm Dia		1 Nos
9			
10			
11			
12			
13			
14			
15			
16			
17			
18			
19			
20			
21			
22			
-23			
24			
25			
26			
27			
28			
#REF!	-		
#REF!	-		
#REF!	-		
#REF!	-		
#REF!	-		

Lowered Assembly in Mtr

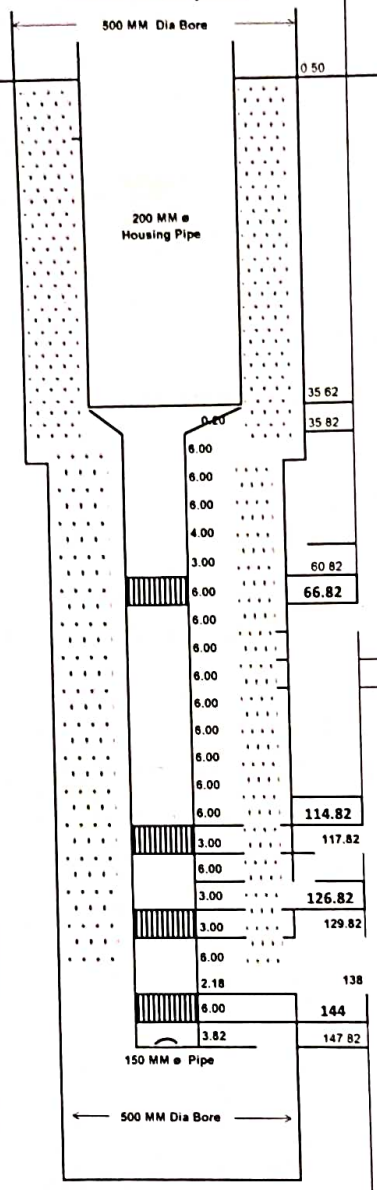

Abstract

1	Required Discharge	: 500	LPM
2	Statice Water Level	: 18.00	M
3	Type of Rig Machine	: R.C / D.C	
4	Bore Size	: 500x500 MM Dia	
5	Assembly size	: 200x150 MM Dia	
6	Drilling Started on Dated	:	
7	Drilling Completed on Dated	:	
8	Drilling Depth	:	
i	500 MM Dia Bore	: 0 to 165 m BGL= 165 M	
ii	450 MM Dia Bore	:	
9	Logging Date	: 27.04.2023	
10	Logging Depth	: 150.00	m bgl
11	Detail of TW Assembly	:	
i	Housing Pipe 200 MM Dia	: 36.12	M
ii	Reducer 200 x 150 MM Dia	: 0.20	M
iii	Plain Pipe 150 MM Dia	: 94.00	M
iv	Slotted Pipe 150 MM Dia	: 18.00	M
	Total	: 148.32	M
	AGL	: 0.50	M
	BGL	: 147.82	M
12	Date of Lowering	:	

Logging Report-27/04/2023

S.No	Depth Range (m bgl)	Thickness (m bgl)	Remarks
1	30.00 - 46.00	16.00 M	Good
2	58.00 - 68.00	10.00 M	Good
3	114.00 - 118.00	4.00 M	Good,Fine sand
4	126.00 - 130.00	4.00 M	Good,Fine sand
5	138.00 - 144.00	6.00 M	Good,Fine sand

Prepared By

M/S RITHWIK KOYA JV

Recommended By

Medhaj Techno Concept Pvt Ltd

J.E.
Division office (E&M), U.P. Jal Nigam (R), Gorakhpur

A.E.

Approved By

E.E.
Division office (E&M), U.P. Jal Nigam (R), Gorakhpur

RITHWIK-KOYA JOINT VENTURE
