GLOBAL GROUND WATER CONSULTANTS

84-III Floor, Humayunpur, Safdarjung Enclave, New Delhi - 110 029
Mobile : 9818 088 824, 9818 007 038
E-mail : srikanthchukka.c23@gamil.com, ravikanth44@yahoo.com

GEOPHYSICAL ELECTRICAL LOGGING REPORT AT

Tubewell No. : .....

Date : 25/04/2022

Village : DULEHRA

Block : SIKANDRABAD

District : Bulandshahar

Depth in Metres	Expected Litholog	Expected Water Quality
0-3	Surface soil	
3-6	Sandy clay	
6-31	Medium Sand	Good
31-37	Sandy clay	
37-67	Medium Sand	Good
67-73	Sandy clay	
73-77	Kankr clay	
77-84	Fine Sand	Good
84-98	Clay Kankar	
98-108	Fine to medium Sand	Good
108-128	Clay Kankar	
128-132	Fine Sand	Good
132-150	Clay	

For Global Groundwater Consultants

(SRIKANTH)

EXPECTED WATER ZONE

WATER LEVEL : .....10 METRES

Consulting Geologists, Geophysists & Ground Water Specialists

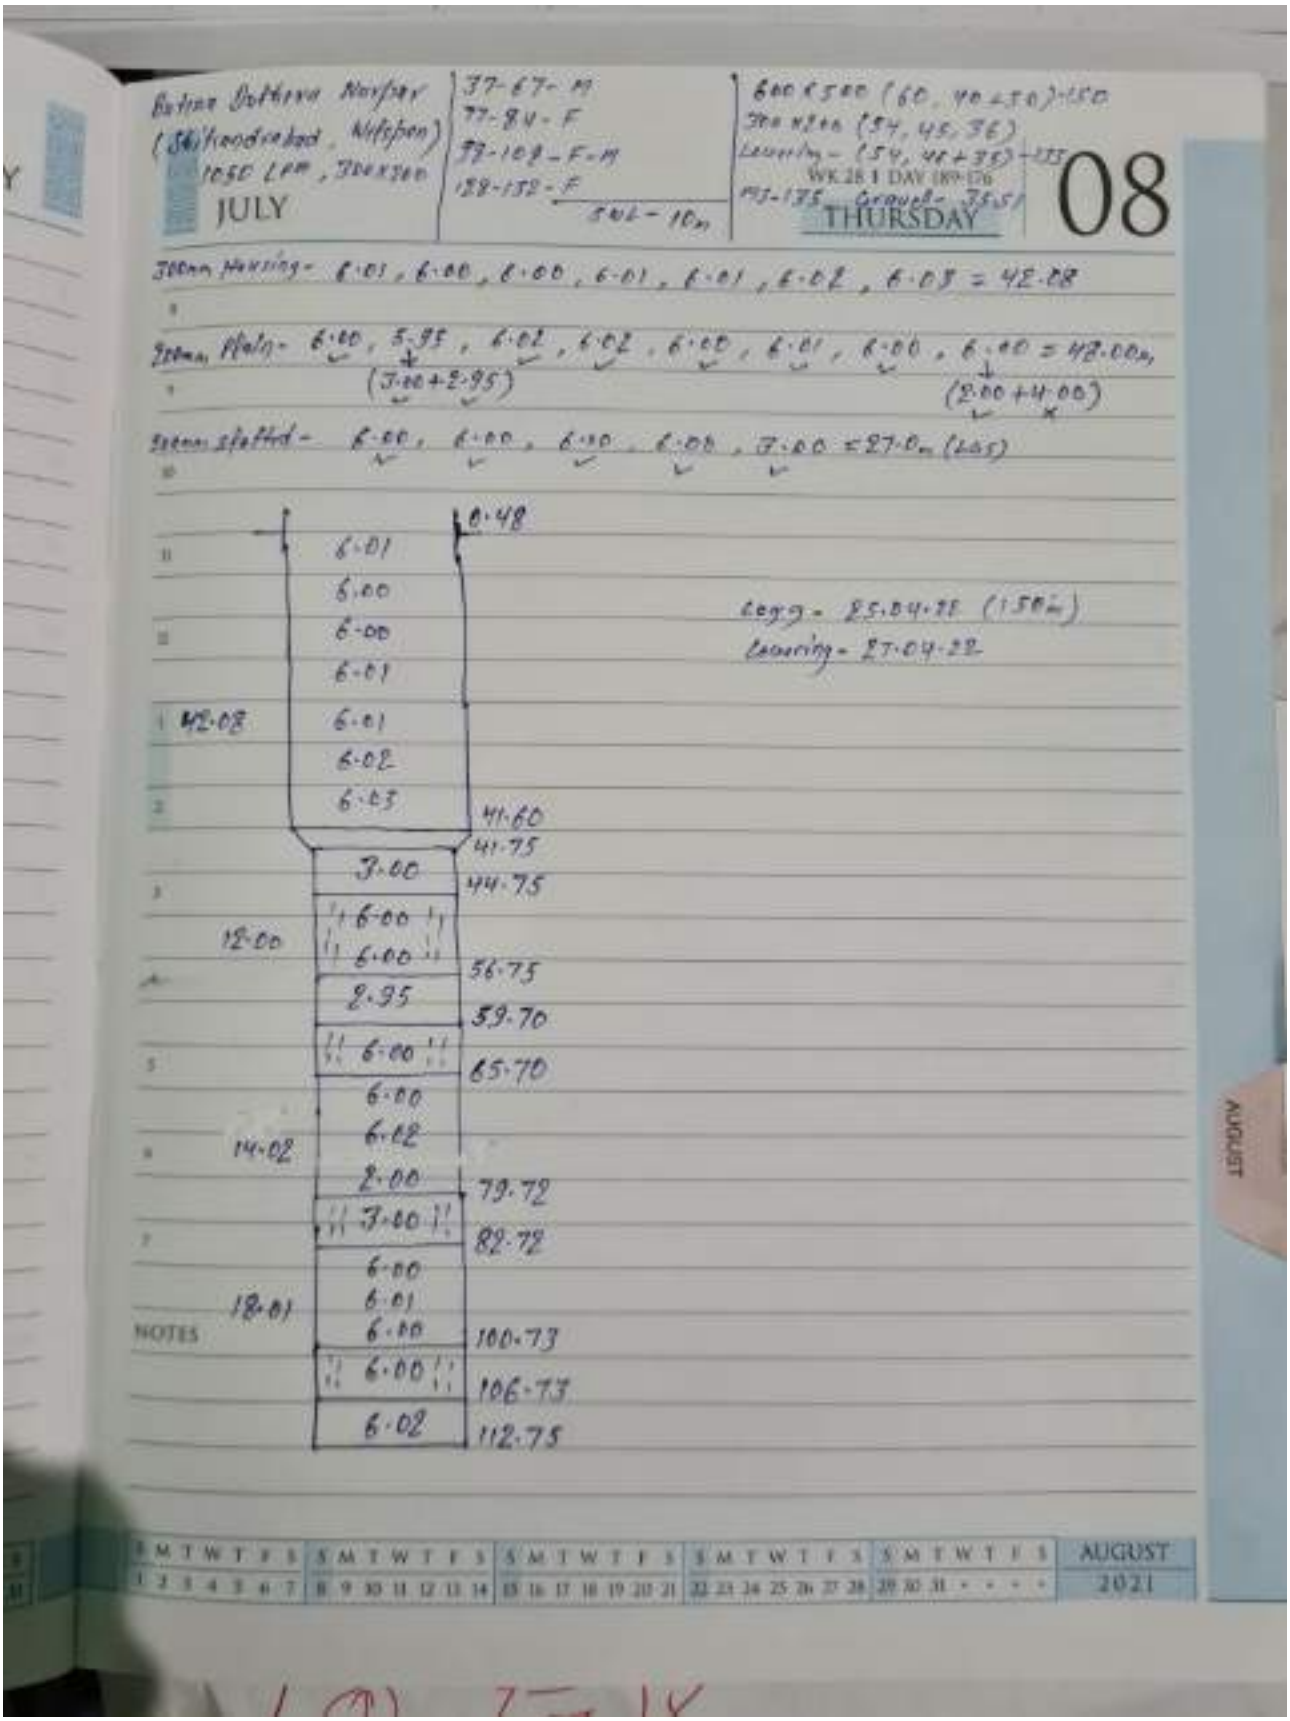
JULY
08
THURSDAY
300mm Housing - 6.01, 6.00, 6.00, 6.01, 6.01, 6.02, 6.03 = 42.08
300mm Main - 6.00, 5.95, 6.02, 6.02, 6.00, 6.01, 6.00, 6.00 = 48.00m
(3.00+2.95)
(2.00+4.00)
300mm slotted - 6.00, 6.00, 6.00, 6.00, 3.00 = 27.0m (245)
0.48
6.01
6.00
6.00
6.01
42.08
6.01
6.02
6.03
41.60
41.75
3.00
44.75
12.00
6.00
6.00
56.75
2.95
59.70
6.00
65.70
6.00
6.02
14.02
2.00
79.72
3.00
82.72
6.00
6.01
18.01
6.00
100.73
6.00
106.73
6.02
112.75
Lay - 25.04.21 (150m)
Laying - 27.04.21
NOTES
AUGUST
2021
