NCC LTD.- GORAKHPUR (UP)

NAME OF THE DISTRICT- Gorakhpur
NAME OF THE BLOCK- Sahjanwa
NAME OF THE GRAM PANCHAYAT- Gangtahi
NAME OF THE VILLAGE-

TYPE OF RIG M/C- RC/DC
SIZE OF BORE- 550 x 500
STATIC WATER LEVEL-
J.E Incharge- A Maurya A.E Incharge- Babban Yadav.

Discharge = 350 LPM

DEPTH B.G.L IN METER	BORING CHART	STRATA
0M		
20.4M		Clay
30.5M		Medium Sand.
56.2M		Sandy clay.
60.6M		Medium to fine Sand.
64.3M		Soft clay
70.7M		Sand With Kanker
72.2M		hard clay.
88.6M		Coarse Sand.
94.1M		clay With Kankar
98.7M		Medium Sand
130.2M		Sandy clay
136.6M		Medium Sand
142.3M		Soft clay
148.8M		Medium Sand
160M		clay.

EXECUTED ASSEMBLY

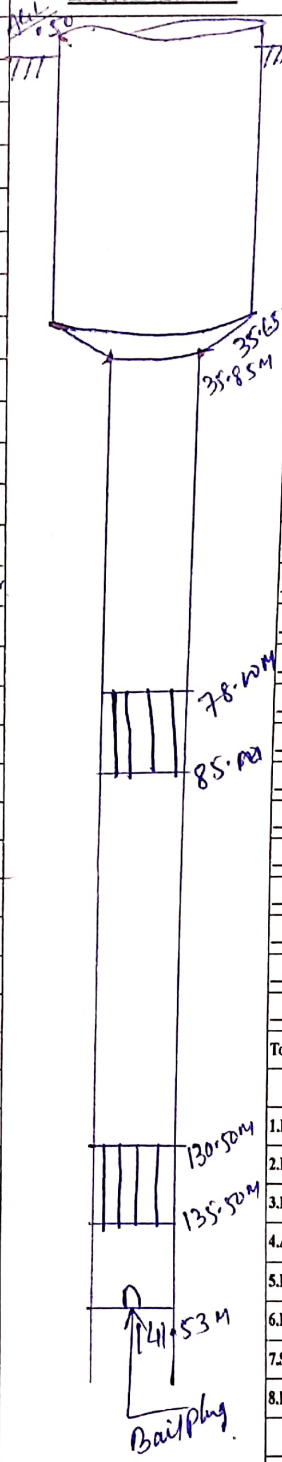

ASSEMBLY DETAILS

200	mm Dia Housing Pipe A.G.L=	0.50	m	
200	mm Dia Housing Pipe	0	m to	35.65 m
200	mm Dia Reducer	35.65	m to	35.85 m
150	mm Dia Blind pipe	35.85	m to	78 m
150	mm Dia Slotted pipe	78	m to	85 m
150	mm Dia Blind pipe	85	m to	130.50 m
150	mm Dia Slotted pipe	130.50	m to	135.50 m
150	mm Dia Blind pipe	135.50	m to	141.53 m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m
	mm Dia pipe		m to	m

Total Assembly= 141.53 m + A.G.L (m) = 142.03 m

ABSTRACT

1.Drilling Started-
2.Drilling Completed/Lowering-
3.Drilling Depth (m)-
4.Assembly Lowered (m)- 142.03
5.Housing Pipe (m)- 36.15
6.Plain Pipe(m)- 93.68
7.Slotted Pipe(m)- 12
8.Reducer(m)- .20,

LOGGING REPORT

1- 20 - 30 = 10M
2- 50 - 60 = 10M
3- 64 - 70 = 6M
4- 72 - 88 = 16M
5- 94 - 98 = 4M
6- 130 - 136 = 6M
7- 142 - 148 = 6M
8-
9-
10-

SOUND TEST-
VERTICALITY TEST-

NCC LTD	J.E & A.E	P.M./C.T.P.I.A	E.E
