NCC LTD.- GORAKHPUR (UP)

NAME OF THE DISTRICT- Gorakhpur.
NAME OF THE BLOCK- Pali
NAME OF THE GRAM PANCHAYAT- Narangpatti
NAME OF THE VILLAGE-

TYPE OF RIG M/C- RC/DC.
SIZE OF BORE- 550 x 500
STATIC WATER LEVEL-
J.E Incharge- A. Narayan A.E Incharge Bubban yadav.

DEPTH B.G.L IN METER	BORING CHART	STRATA
0M		Sandy clay
22.3M		Medium to fine Sand.
30.4M		Soft clay.
42.2M		Medium Sand.
63.6M		hard clay.
66.3M		coarse Sand.
74.5M		clay With Kankar.
93.2M		Medium Sand.
100.7M		Soft clay
116.3M		Medium Sand.
120.5M		Sandy clay With kankar.
136.2M		Medium Sand
140.6M		clay.
165M		

EXECUTED ASSEMBLY

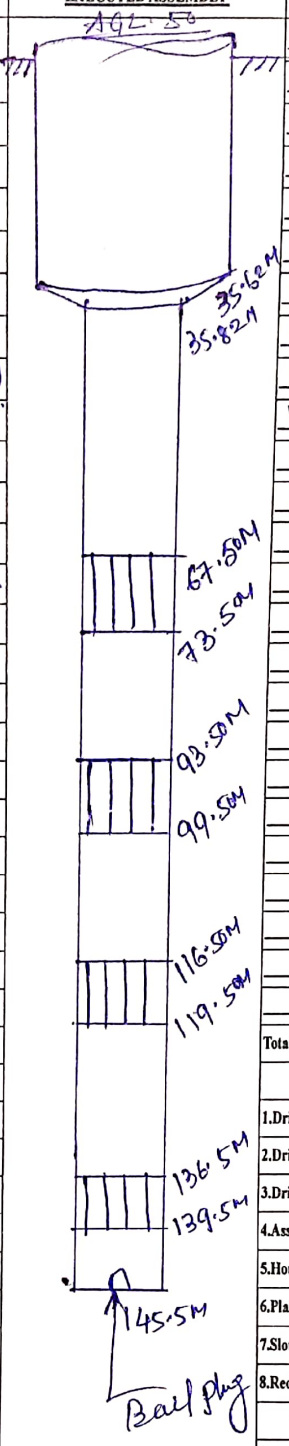

ASSEMBLY DETAILS

200 mm Dia Housing Pipe A.G.L= 0.50 m
200 mm Dia Housing Pipe 0 m to 35.62 m
200 mm Dia Reducer 35.62 m to 35.82 m
150 mm Dia Blind pipe 35.82 m to 67.50 m
150 mm Dia Slotted pipe 67.50 m to 73.50 m
150 mm Dia Blind pipe 73.50 m to 93.50 m
150 mm Dia Slotted pipe 93.50 m to 99.50 m
150 mm Dia Blind pipe 99.50 m to 116.50 m
150 mm Dia Slotted pipe 116.50 m to 119.50 m
150 mm Dia Blind pipe 119.50 m to 136.50 m
150 mm Dia Slotted pipe 136.50 m to 139.50 m
150 mm Dia Blind pipe 139.50 m to 145.50 m
_____ mm Dia _____ pipe _____ m to _____ m
_____ mm Dia _____ pipe _____ m to _____ m
_____ mm Dia _____ pipe _____ m to _____ m
_____ mm Dia _____ pipe _____ m to _____ m
_____ mm Dia _____ pipe _____ m to _____ m
_____ mm Dia _____ pipe _____ m to _____ m
_____ mm Dia _____ pipe _____ m to _____ m
_____ mm Dia _____ pipe _____ m to _____ m
_____ mm Dia _____ pipe _____ m to _____ m
_____ mm Dia _____ pipe _____ m to _____ m
_____ mm Dia _____ pipe _____ m to _____ m
_____ mm Dia _____ pipe _____ m to _____ m
Total Assembly= 145.50 m + A.G.L (m) = 146 m

ABSTRACT

1.Drilling Started-
2.Drilling Completed/Lowering-
3.Drilling Depth (m)-
4.Assembly Lowered (m)- 146
5.Housing Pipe (m)- 36.12
6.Plain Pipe(m)-
7.Slotted Pipe(m)- 18
8.Reducer(m)- .20

LOGGING REPORT

1-
2-
3-
4-
5-
6-
7-
8-
9-
10-

SOUND TEST-
VERTICALITY TEST-

NCC LTD	J.E & A.E	P.M./C/T.P.I.A	E.E
_____	_____	_____	_____
