SWSM/DWSM

NCC LTD.- GORAKHPUR (UP)

NAME OF THE DISTRICT- Gorakhpur.
NAME OF THE BLOCK- Campierganj
NAME OF THE GRAM PANCHAYAT- Bargadahi
NAME OF THE VILLAGE-

TYPE OF RIG M/C- RC/DC
SIZE OF BORE- 600x500
STATIC WATER LEVEL-
J.E Incharge- A. Maurya A.E Incharge- Bathan yadav

Discharge- 750LPM

DEPTH B.G.L IN METER	BORING CHART	STRATA
0M		Sandy clay.
21.4M		Medium Sand.
30.5M		Clay With Kankar.
81.3M		Medium Sand.
87.6M		Soft clay.
93.2M		Medium Sand.
102.7M		Sandy clay.
121.9M		Medium Sand.
136.6M		Hard clay.
144.2M		Medium Sand.
152.5M		Clay With Kankar.
168.3M		Coarse Sand.
182.6M		Sandy clay.
186.2M		Medium Sand.
199.7M		clay.
220M		

EXECUTED ASSEMBLY

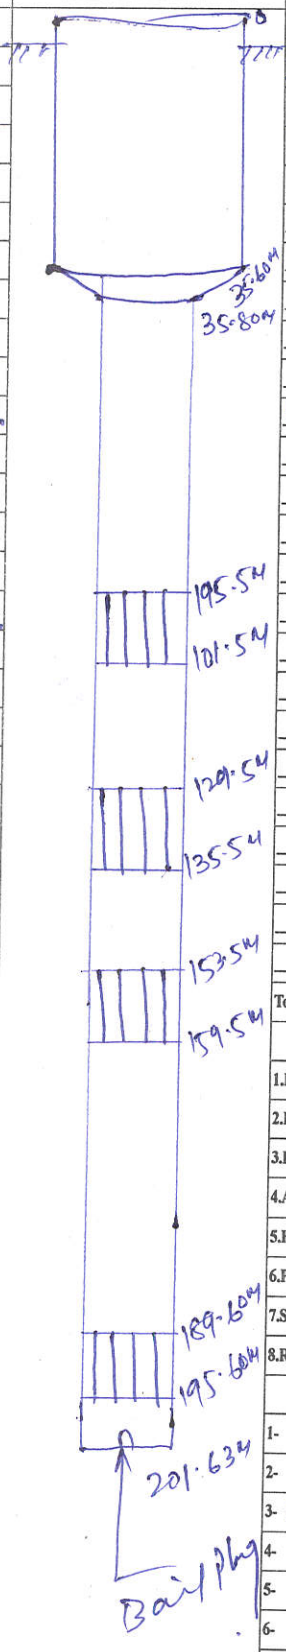

ASSEMBLY DETAILS

350	mm Dia	Housing Pipe A.G.L=	.50	m
300	mm Dia	Housing Pipe	0 m to 35.60	m
300	mm Dia	Reducer	35.60 m to 35.80	m
150	mm Dia	Blind pipe	35.80 m to 95.5	m
150	mm Dia	Slotted pipe	95.5 m to 101.5	m
150	mm Dia	Blind pipe	101.5 m to 129.5	m
150	mm Dia	Slotted pipe	129.5 m to 135.5	m
150	mm Dia	Blind pipe	135.5 m to 153.5	m
150	mm Dia	Slotted pipe	153.5 m to 159.5	m
150	mm Dia	Blind pipe	159.5 m to 189.6	m
150	mm Dia	Slotted pipe	189.6 m to 195.6	m
150	mm Dia	Blind pipe	195.6 m to 201.63	m

Total Assembly= 201.63 m + A.G.L (m) = 202.13 m

ABSTRACT

1.Drilling Started-
2.Drilling Completed/Lowering- 09/04/024
3.Drilling Depth (m)- 220 M.
4.Assembly Lowered (m)- 202.13
5.Housing Pipe (m)- 36.10
6.Plain Pipe(m)- 141.83.
7.Slotted Pipe(m)- 24.
8.Reducer(m)- .20

LOGGING REPORT

1- 21 - 30 = 9M
2- 81 - 87 = 6M
3- 93 - 102 = 9M
4- 121 - 136 = 15M
5- 144 - 162 = 18M
6- 168 - 182 = 14M
7- 186 - 199 = 13M.
8-
9-
10-

SOUND TEST-
VERTICALITY TEST-

NCC LTD	J.E & A.E	P.M.C/T.P.I.A	E.E
