# EXECUTIVE ENGINEER TEMP. CONSTRUCTION DIVISION (E/M), U.P. JAL NIGAM, MORADABAD

**Completion Plan of Tube well**

**Name of Scheme:-** Tumariya Rural Water Supply Scheme Distt. Rampur

**Total No. of Tube well Provided in the Scheme:-** 01

**Number & Location of tube-well Executed:-** Near Over Head Tank

**Name of Contractor:-** M/s A.S.L. Enterprises Meerut

**Type of Rig M/c:-** R.C. 600/27"

**Static water level:-** 6.40 Mtr

**Size of Bore:-** 675 X 600 mm

**Date of Completion of T.W.** -12.03.2015

| Depth B. G. Meter | Boring Chart | Stratam |
|---|---|---|
| 4.57 | | Surface clay |
| 10.67 | | Fine Sand |
| | | Fine To Medium Sand, |
| 32.00 | | |
| 38.10 | | clay |
| 47.24 | | Very Fine Sand |
| | | clay |
| 65.53 | | |
| | | Medium To Course Sand, |
| 80.77 | | |
| 83.81 | | clay |
| 96.00 | | Very Fine Sand |
| | | Kankar clay |
| 99.00 | | |
| | | medium to Course Sand |
| 114.30 | | |
| | | clay |
| 123.44 | | |

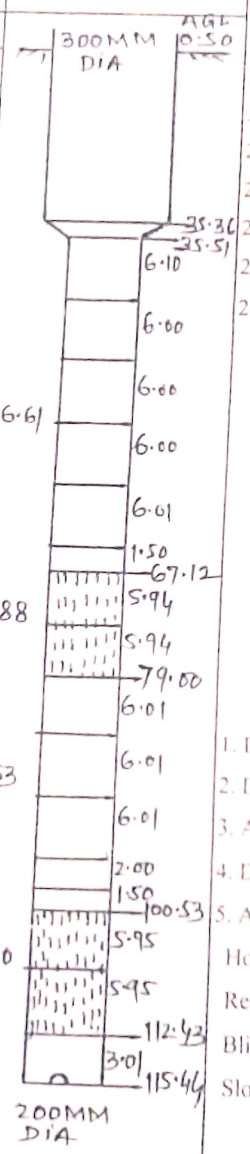


**ASSEMBLY DETAILS**

300 m.m. Dia Housing pipe G.L. m to 0.50 m A.G.L.
300 m.m. Dia Housing pipe G.L. m to 35.36 m B.G.
300 X 200 m.m. Dia Reducer 35.36 m to 35.11 m.
200 m.m. Dia Blind pipe 35.11 m to 67.12 m.
200 m.m. Dia Slotted pipe 67.12 m to 79.00 m.
200 m.m. Dia Blind pipe 79.00 m to 100.53 m.
200 m.m. Dia Slotted pipe 100.53 m to 112.43 m.
200 m.m. Dia Blind pipe 112.43 m to 115.44 m.

**ABSTRACT**

| | | |
|---|---|---|
| 1. Drilling Started on | - | 06.02.2015 |
| 2. Drilling Completed on | - | 11.02.2015 |
| 3. Assembly Lowered on | - | 12.02.2015 |
| 4. Drilling Depth | - | 123.44 m |
| 5. Assembly Lowered | - | 115.94 m |
| Housing Pipe 300 m.m. dia | - | 35.86 m |
| Reducer 300x200 m.m. dia | - | 0.15 m |
| Blind Pipe 200 m.m. dia | - | 56.15 m |
| Slotted Pipe 200 m.m. dia | - | 23.78 m |

As Executed

Ajay
(M/s A.S.L. Enterprises Meerut)
Contractor

(Santosh Kumar)
J.E.

(Mohd. Maaz)
A.E.

Countersigned

(M.K. Bhatia)
Executive Engineer

D:\Shreta Cham\Tumariya xls\Sheet10

Scanned with OKEN Scanner
