JJM-01

OFFICE OF THE EXECUTIVE ENGINEER 2nd CD (E/M) UTTAR PRADESH JAL NIGAM PRAYAGRAJ

Actual ASSEMBLY / STRATA CHART OF TUBE WELL **PATTI NARWAR(NASIRPUR)** BLOCK MOORATGANJ
WATER SUPPLY SCHEME UNDER JAL JEEVAN MISSION KAUSHAMBI

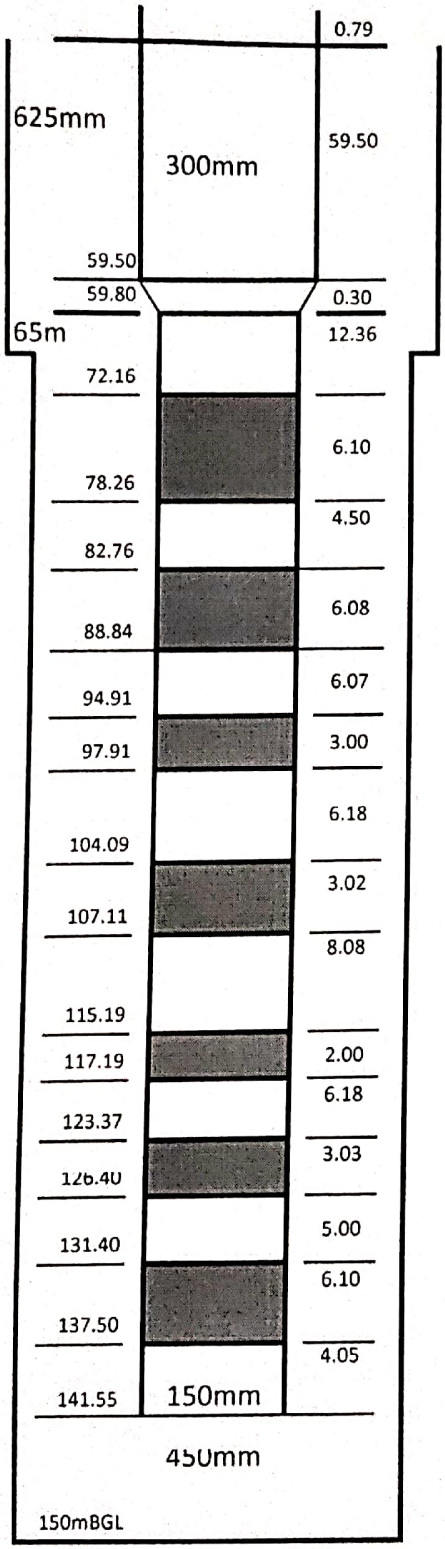

1	Tubwe Well Constructed by	M/S Narayan Singh Chandraul
2	Drilling Started On	29.08.2020
3	Drilling Completed On	18.09.2020
4	Assy Lowered on	18.09.2020
5	Size of Bore Well	625mm & 450mm
6	Pea Gravel Feed	18.09.2020

LOGGING DETAILS		
1	Logging Date	04.09.2020
2	Logged/Drilled Depth	140mBGL/140mBGL
3	Logging By	Mr Gaurav Shukla Asst Hydrogeologist

1	38-49	11 M Good
2	72-79	7 m Good
3	82-89	7 m Good
4	94-98	4 m Good
5	104-108	4 m Good
6	115-118	3 m Good
7	123-127	4 m Good
8	131-138	7 m Good
	Required Discharge	**1100 LPM**

Contractor Computor Junior Engg Asst Engg Executive Engg
